




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348



Sedona in Motion 1B – Uptown Northbound Improvements

FY22 CIP Update

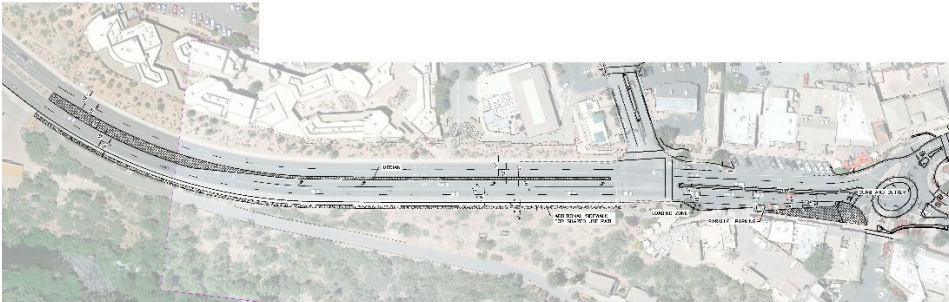

KEY FEATURES:

Consultant: Kimley-Horn

Contractor: TBD

Timing: March 2021 – June 2022

Construction Challenges:

- Heavy vehicular and pedestrian traffic
- Traffic Control

Project Manager:

Stephen Craver, PE
 (928) 203-5059

SCraver@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039

ADickey@SedonaAZ.gov

\$ FY22 Project Budget: \$460,000

Total Project Budget: \$535,000

While southbound delay has been drastically reduced with the completion of SIM-01, northbound congestion appears to have worsened. This project will provide further data collection, modeling, and analysis to identify strategies that will help alleviate northbound congestion through Uptown that often spills back to the "Y" roundabout and creates congestion for northbound SR 179, and northbound SR 89A coming down Cooks Hill. Construction budget is included in FY 2022 for projects that may result from the analysis.

Status: Extensive data collection was done on March 20, 2021. The consultant has utilized that data to update the existing conditions model. They are now working on modeling various improvement alternatives and will provide recommendations by the end of September. These recommendations will be presented to Council at the October 13 work session.

For a copy of this update, or updates for other projects, visit the projects website at: www.sedonaaz.gov/CIP.

Project Status

August 2021

Project Phase	% Completion	Completion Date
Design	70%	November 2021
Construction	0%	TBD
