




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

SD-12 - Schnebly & Grove Drainage Improvements

FY23 CIP Update

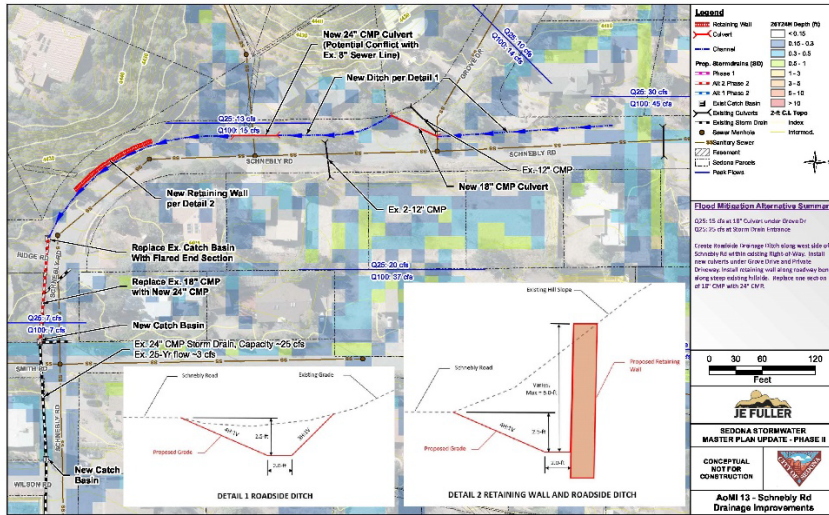

KEY FEATURES:

Consultant: JE Fuller

Contractor: TBD

Timing: FY23 Design; FY24 Construction

Construction Challenges:

- Limited right-of-way
- Maintain traffic flow
- Accommodate increased runoff due to build-out in the area

Project Manager:

Sandra Phillips, PE, CFM
 (928) 203-0118
SPhillips@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039
ADickey@SedonaAZ.gov

\$ FY23 Project Budget: \$272,700
Total Project Budget: \$424,200

Residents requested that the City review options to help alleviate drainage concerns in this area. Substantial flooding occurs in the area during monsoons. Infrastructure is well under capacity now that this area is built out.

Development of plans, specifications, and cost estimate to intercept and direct flows down Schnebly Road into existing infrastructure. This is a project created from the outreach to residents through the Stormwater Master Plan Update.

Consultant, JE Fuller, has been awarded the contract and begun pulling past documents to start design.

Project Status

December 2022

Project Phase	% Completion	Completion Date
Design	10%	Spring 2023
Construction	0%	Winter 2023
