




**City of Sedona**  
**Public Works Department**  
 102 Roadrunner Drive Sedona, AZ 86336  
 (928) 204-7111 • Fax: (928) 282-5348

**SD-12 - Schnebly & Grove Drainage Improvements**

**FY23 CIP Update**

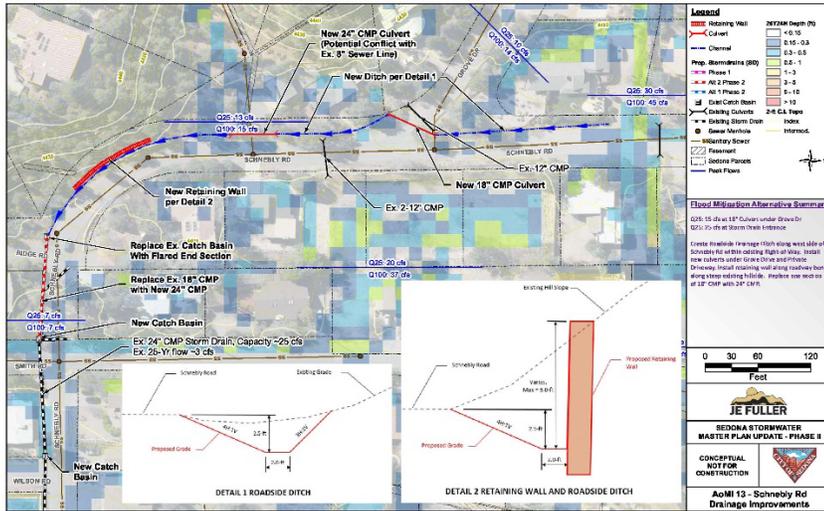

**KEY FEATURES:**

**Consultant:** JE Fuller

**Contractor:** TBD

**Timing:** FY23 Design; FY24 Construction

**Construction Challenges:**

- Limited right-of-way
- Maintain traffic flow
- Accommodate increased runoff due to build-out in the area

**Project Manager:**

Sandra Phillips, PE, CFM  
 (928) 203-0118  
[SPhillips@SedonaAZ.gov](mailto:SPhillips@SedonaAZ.gov)

**City Engineer:**

J. Andy Dickey, PE  
 (928) 203-5039  
[ADickey@SedonaAZ.gov](mailto:ADickey@SedonaAZ.gov)

**\$ FY23 Project Budget:** \$272,700  
**Total Project Budget:** \$424,200

Residents requested that the City review options to help alleviate drainage concerns in this area. Substantial flooding occurs in the area during monsoons. Infrastructure is well under capacity now that this area is built out.

Development of plans, specifications, and cost estimate to intercept and direct flows down Schnebly Road into existing infrastructure. This is a project created from the outreach to residents through the Stormwater Master Plan Update.

Consultant, JE Fuller, has been awarded the contract and begun pulling past documents to start design. Survey is complete and design is underway. Potholing to be done.

**Project Status**

**April 2023**

Project Phase	% Completion	Completion Date
Design	30%	Sumer 2023
Construction	0%	Winter 2023
