




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

WW-01F - Major Lift Station Upgrades

FY24 CIP Update

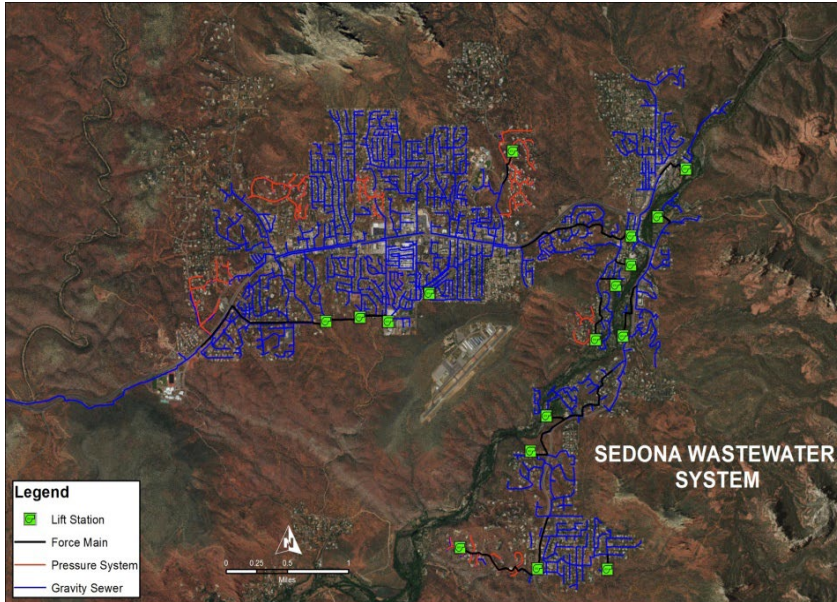

KEY FEATURES:

Consultant: Carollo Engineers, Inc.

Contractor: KEAR Civil Corporation

Timing: FY21-FY25

Construction Challenges:

- Potential by-pass operations
- Maintaining operations of the lift stations
- Equipment procurement lead times

Project Manager:

Roxanne Holland, PE

(928) 203-5069

RHolland@SedonaAZ.gov

City Engineer:

Kurtis Harris, PE

(928) 203-5059

KHarris@SedonaAZ.gov

\$ FY24 Project Budget: \$3,668,985

Total Project Budget: \$6,858,500

The Major Lift Station Upgrades project will make improvements at the three major lift stations; Brewer Rd., Carroll Canyon, and El Camino lift stations. Work will consist of upgrading obsolete controls, allowing for efficient and reliable automation. Additionally, coatings will be refreshed in the wet wells, and variable frequency drives, flow meters, and transfer switches will be replaced.

Status: KEAR Civil Corporation has mobilized and begun work on the lift station upgrades. Work has started at the Brewer Lift Station on installing new pumps and variable frequency drives. The project is anticipated to be complete in December 2024.

Project Status **January 2024**

Project Phase	% Completion	Completion Date
Design	100%	May 2022
Construction	5%	December 2024
