




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

Major Lift Station Upgrades

FY22 CIP Update

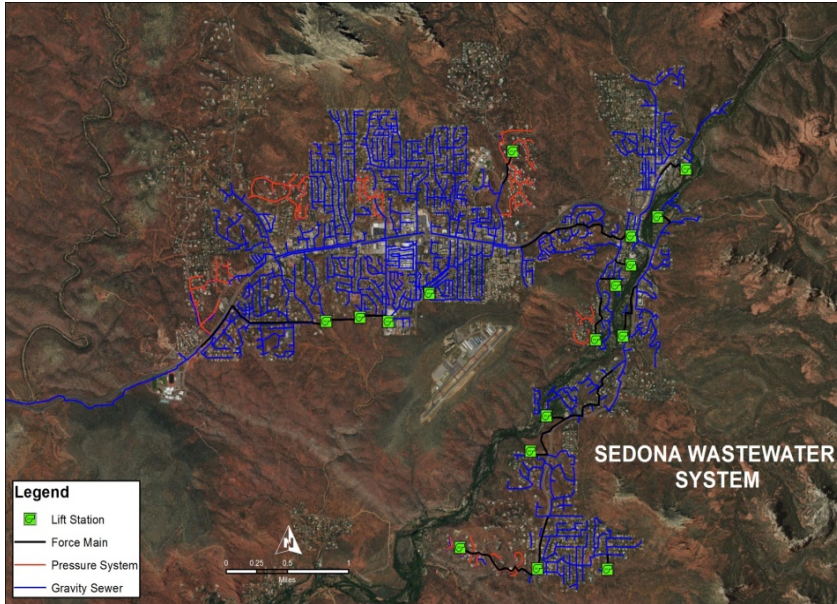

KEY FEATURES:

Consultant: Carollo Engineers, Inc.

Contractor: TBD

Timing: Spring 2021

Construction Challenges:

- Potential by-pass operations
- Maintaining operations of the lift stations

Project Manager:

Roxanne Holland, PE
 (928) 203-5069

RHolland@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039

ADickey@SedonaAZ.gov

\$ FY22 Project Budget: \$1,102,000
Total Project Budget: \$1,132,000

The Major Lift Station Upgrades project will make improvements at the three major lift stations; Brewer Rd., Carroll Canyon, and El Camino lift stations. Work will consist of upgrading obsolete controls, allowing for efficient and reliable automation. Additionally, coatings will be refreshed in the wet wells, and variable frequency drives, flow meters, and transfer switches will be replaced. Design of the upgrades will begin in Fiscal Year 2021, and construction is proposed in Fiscal Year 2022

Status: Carollo Engineers completed the 50% design milestone ahead of schedule and staff is currently reviewing those plans. A Construction Manager at Risk contract is currently advertised to add a contractor to the project team prior to completion of the design. A contractor will be selected in January, with a contract going to City Council for approval in February.

For a copy of this update, or updates for other projects, visit the projects website at: www.sedonaaz.gov/CIP.

Project Status

November 2021

Project Phase	% Completion	Completion Date
Design	50%	Winter 2021
Construction	0%	Winter 2021/2022
