




Sedona in Motion 5C – Los Abridados to Brewer Connection

FY22 CIP Update

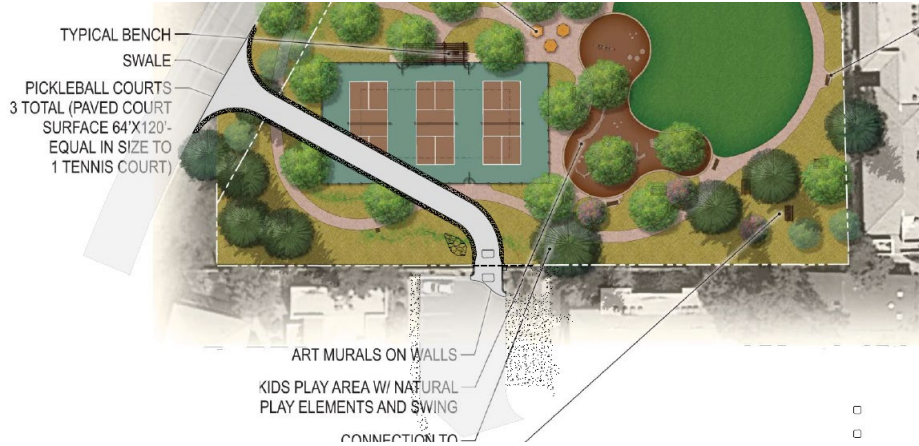

KEY FEATURES:

Consultant: Shephard-Wesnitzer (SWI)

Contractor: TBD

Timing: October 2020 – FY 22

Construction Challenges:

Project Manager:

Stephen Craver, PE
 (928) 203-5059

SCraver@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039

ADickey@SedonaAZ.gov

\$ FY22 Project Budget: \$150,000

Total Project Budget: \$163,050

This project is a result of the Transportation Master Plan. It will provide a connection from Los Abridados through the City owned Ranger Station property to Brewer Road. It provides a similar benefit as SIM-5A as it will further reduce the number of vehicles needing to make a U-turn at the Schnebly Hill roundabout, which will reduce congestion and improve travel time for northbound SR 179.

Status: Design for this project began in October 2020 and was completed in August 2021. Prior to finalizing design, the concept was presented to the Historic Preservation Commission on May 10, and the Planning and Zoning Commission on June 1. Both approved an amendment to the Ranger Station Park Master Plan which will now remove the pickleball courts. Staff has coordinated with Los Abridados to formalize their committed cost share. The cost-share agreement will be presented to Council at the February 8, 2022 meeting. Once approved, staff will move forward with advertising for construction in mid-February.

For a copy of this update, or updates for other projects, visit the projects website at: www.sedonaaz.gov/CIP.

Project Status

January 2022

Project Phase	% Completion	Completion Date
Design	100%	August 2021
Construction	0%	June 2022
