




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

Major Lift Station Upgrades

FY22 CIP Update

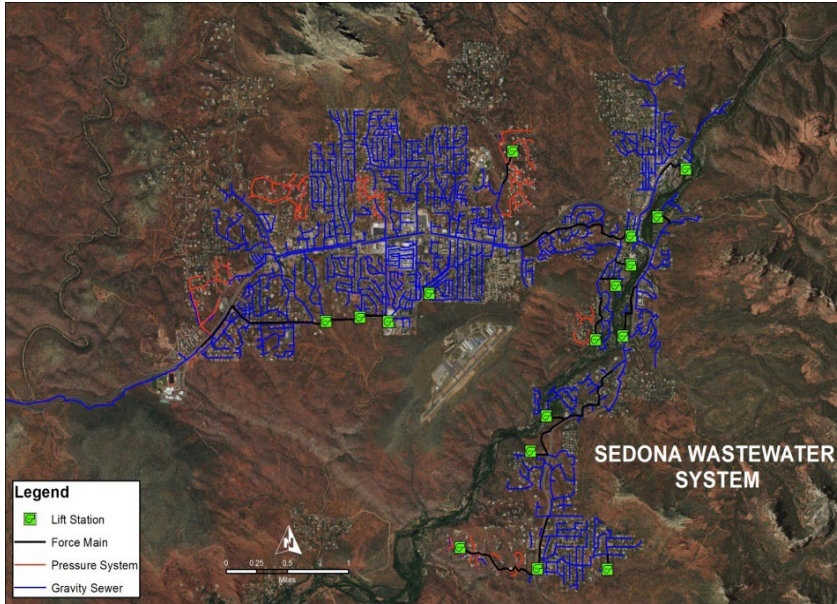

KEY FEATURES:

Consultant: Carollo Engineers, Inc.

Contractor: KEAR Civil Corporation

Timing: Spring 2021

Construction Challenges:

- Potential by-pass operations
- Maintaining operations of the lift stations
- Equipment procurement lead times

Project Manager:

Roxanne Holland, PE

(928) 203-5069

RHolland@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE

(928) 203-5039

ADickey@SedonaAZ.gov

\$ FY22 Project Budget: \$1,102,000

Total Project Budget: \$5,200,000

The Major Lift Station Upgrades project will make improvements at the three major lift stations; Brewer Rd., Carroll Canyon, and El Camino lift stations. Work will consist of upgrading obsolete controls, allowing for efficient and reliable automation. Additionally, coatings will be refreshed in the wet wells, and variable frequency drives, flow meters, and transfer switches will be replaced. Design of the upgrades will begin in Fiscal Year 2021, and construction is proposed in Fiscal Year 2022

Status: Carollo Engineers have completed the 90% design milestone. A staff evaluation committee reviewed Statements of Qualifications from Contractors wishing to complete the construction and selected KEAR Civil Corporation as the top-rated contractor. KEAR is currently developing a design phase services scope of work to provide input on the 90% design plans. Upon final completion of the design phase, a construction phase services contract is anticipated to be presented to City Council for approval in the spring.

For a copy of this update, or updates for other projects, visit the projects website at: www.sedonaaz.gov/CIP.

Project Status

January 2022

Project Phase	% Completion	Completion Date
Design	90%	Winter 2021
Construction	0%	Spring 2023
