




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

Juniper Trail Sewer Extension

FY22 CIP Update

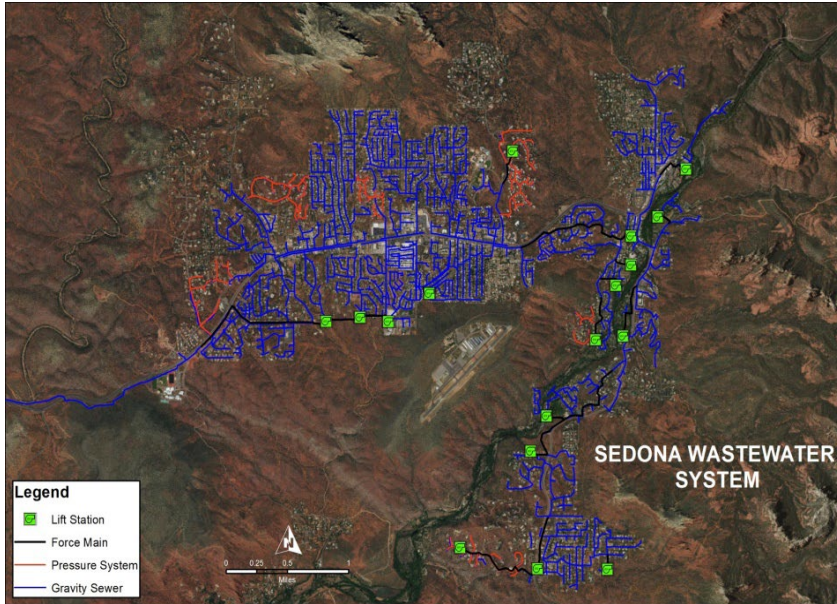

KEY FEATURES:

Consultant: Shephard-Wesnitzer, Inc.

Contractor: KEAR Civil Corporation

Timing: Spring/Summer 2022

Construction Challenges:

- Potential for repair of dryline

Project Manager:

Roxanne Holland, PE
 (928) 203-5069

RHolland@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039

ADickey@SedonaAZ.gov

\$ FY22 Project Budget: \$60,000

Total Project Budget: \$60,000

In 2011, in conjunction with the SR179 Realignment Project, an 8-inch dryline sewer was installed for future use. In order to make the dryline active, approximately 200 linear feet of sewer will be installed in Juniper Trail to tie the dryline into the active collection system. The extension will allow for the potential connection of up to 31 properties, 9 of which are undeveloped.

Status: Shephard-Wesnitzer, Inc. has completed the design of the new sewer main. A construction contract with KEAR Civil Corporation is scheduled for approval at the July 12, 2022 City Council meeting. Construction on the project will begin mid-July and will take approximately 3 months to complete.

For a copy of this update, or updates for other projects, visit the projects website at: www.sedonaaz.gov/CIP.

Project Status

June 2022

Project Phase	% Completion	Completion Date
Design	100%	Winter 2021/2022
Construction	0%	Summer 2022
