




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

WW-01H - Juniper Trail Sewer Extension

FY23 CIP Update

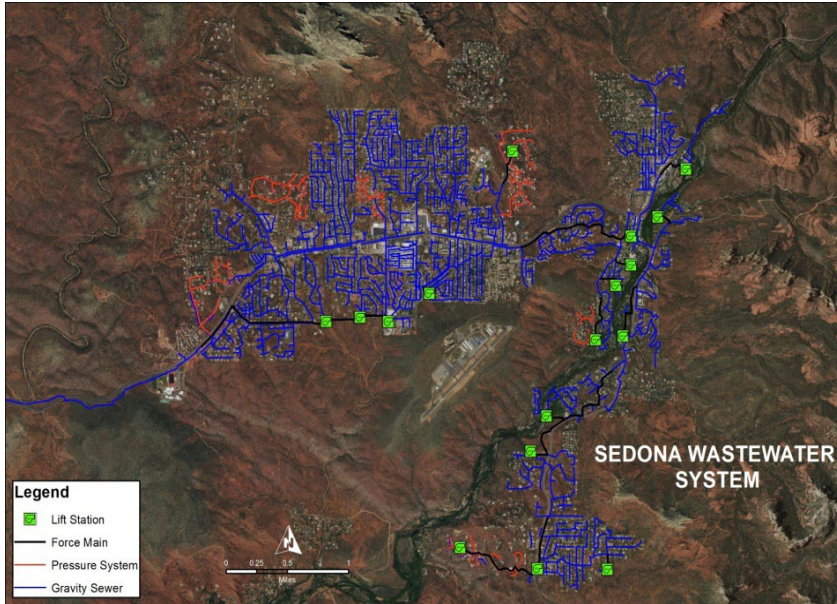

KEY FEATURES:

Consultant: Shephard-Wesnitzer, Inc.

Contractor: KEAR Civil Corporation

Timing: Summer/Fall 2022

Construction Challenges:

- Potential for repair of dryline

Project Manager:

Roxanne Holland, PE
 (928) 203-5069

RHolland@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039

ADickey@SedonaAZ.gov

\$ FY23 Project Budget: \$170,000

Total Project Budget: \$180,520

In 2011, in conjunction with the SR179 Realignment Project, an 8-inch dryline sewer was installed for future use. In order to make the dryline active, approximately 200 linear feet of sewer will be installed in Juniper Trail to tie the dryline into the active collection system. The extension will allow for the potential connection of up to 31 properties, 9 of which are undeveloped.

Status: KEAR Civil Corporation has completed trench excavation and installation of approximately 50% of the new sewer pipe. Crews will complete the pipe installation and establish new sewer services, prior to repaving the roadway. Construction is anticipated to be complete in October 2022.

Project Status

August 2022

Project Phase	% Completion	Completion Date
Design	100%	Winter 2021/2022
Construction	60%	Summer/Fall 2022
