




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

Sedona in Motion 11E - Navoti Dr to Dry Creek Rd SUP

FY23 CIP Update

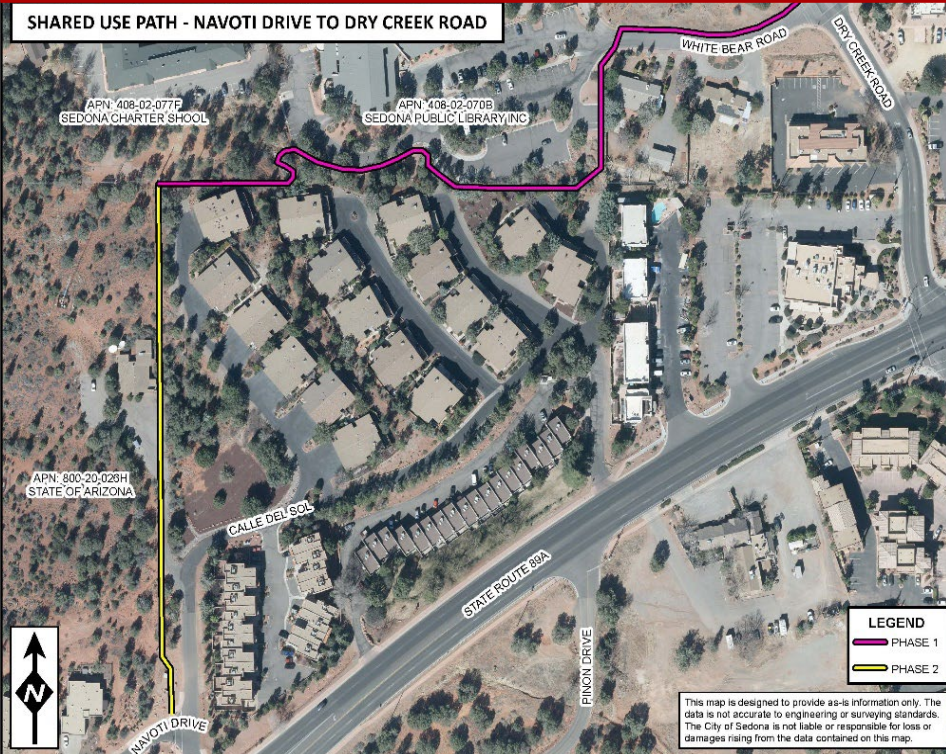

KEY FEATURES:

Consultant: Shephard Wesnitzer, Inc.

Contractor: Standard Construction Co

Timing: FY 23

Construction Challenges:

Maintenance of traffic
 Fitting within existing parking lot

Project Manager:

James Crowley EIT, RLS
 (928) 203-5092
JCrowley@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039
ADickey@SedonaAZ.gov

\$ FY23 Project Budget: \$800,000
Total Project Budget: \$824,000

The Transportation Master Plan, Strategy 11, Walking and Bicycling Facilities, indicates that these improvements collectively encourage use of alternative modes of travel in Sedona, and support a park-once culture where visitors and residents are encouraged to leave their vehicles at their place of lodging/residence. To have a measurable impact on traffic congestion, shared-use path connections will be required.

This project would provide a shared-use pathway connection from Navoti Drive to White Bear Road and Dry Creek Road. This will also provide a multimodal connection to western Sedona/Red Rock High School other than SR 89A.

Break out of Phase 1 includes portion of shared-use path from Dry Creek Road to back side of the Library in FY 2023. Remaining portion of the trail in Phase 2 is dependent upon easements from property owners and to be completed in FY 2024.

The construction contract with Summit Construction was approved by city council and the shared-use path is under construction. Access to the Sedona Public Library will remain open during the improvement project.

Project Status

December 2022

Project Phase	% Completion	Completion Date
Design	100%	Summer 2022
Construction	50%	Summer 2023
