




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

SD-12 - Schnebly & Grove Drainage Improvements

FY23 CIP Update

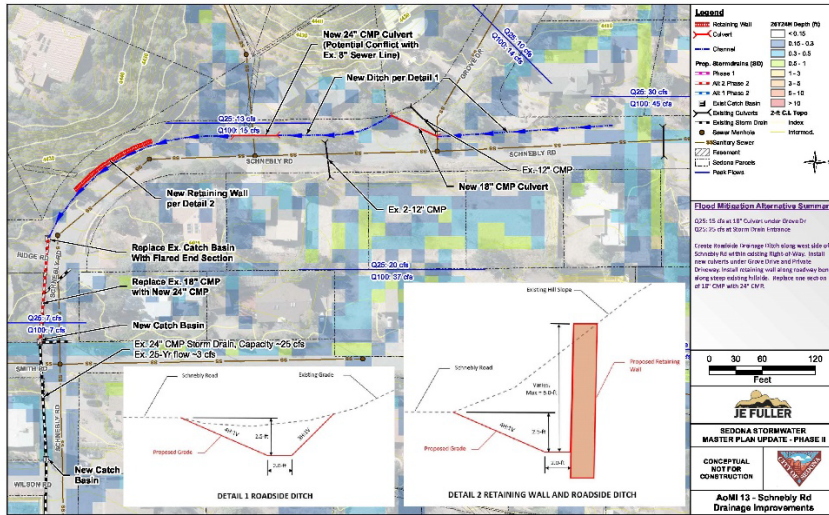

KEY FEATURES:

- Consultant:** JE Fuller
- Contractor:** TBD
- Timing:** FY23 Design; FY24 Construction
- Construction Challenges:**

Limited right-of-way
 Maintain traffic flow
 Accommodate increased runoff due to build-out in the area

Project Manager:
 Sandra Phillips, PE, CFM
 (928) 203-0118
SPhillips@SedonaAZ.gov

City Engineer:
 J. Andy Dickey, PE
 (928) 203-5039
ADickey@SedonaAZ.gov

\$ FY23 Project Budget: \$272,700
Total Project Budget: \$424,200

Residents requested that the City review options to help alleviate drainage concerns in this area. Substantial flooding occurs in the area during monsoons. Infrastructure is well under capacity now that this area is built out.

Development of plans, specifications, and cost estimate to intercept and direct flows down Schnebly Road into existing infrastructure. This is a project created from the outreach to residents through the Stormwater Master Plan Update.

Consultant, JE Fuller, has been awarded the contract and begun pulling past documents to start design. Survey is complete and design is underway. Potholing to be done.

Project Status		February 2023	
Project Phase	% Completion	Completion Date	
Design	15%	Sumer 2023	
Construction	0%	Winter 2023	
