




**City of Sedona**  
**Public Works Department**  
 102 Roadrunner Drive Sedona, AZ 86336  
 (928) 204-7111 • Fax: (928) 282-5348

**Sedona in Motion 11E - Navoti Dr to Dry Creek Rd SUP**

**FY24 CIP Update**

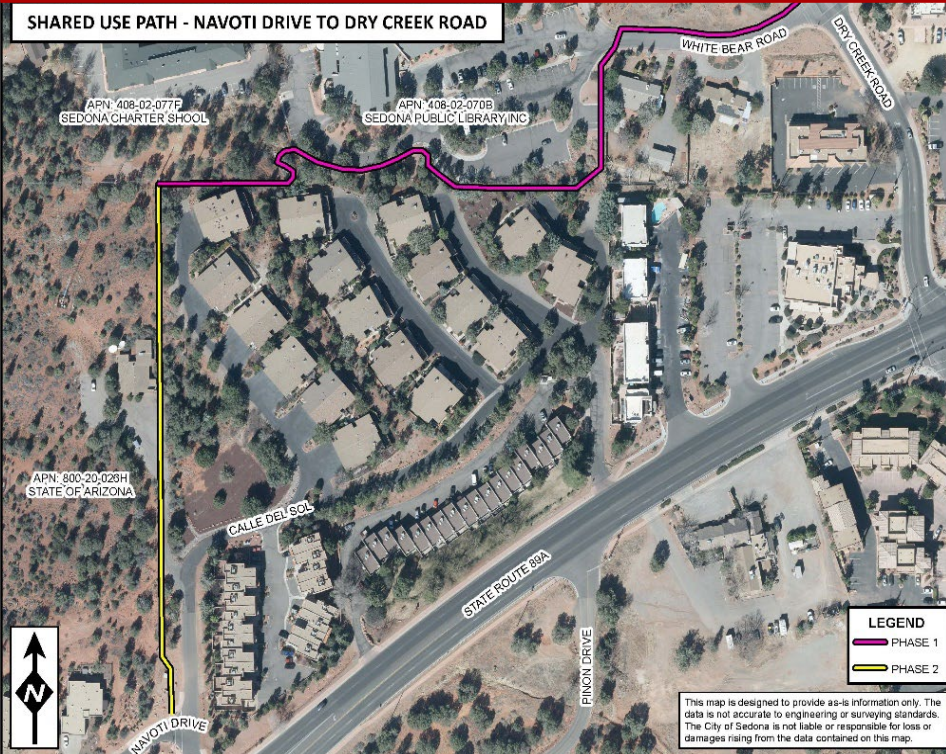

**KEY FEATURES:**

**Consultant:** Shephard Wesnitzer, Inc.

**Contractor:** Standard Construction Co

**Timing:** Through FY25

**Construction Challenges:**

Maintenance of traffic  
 Fitting within existing parking lot

**Project Manager:**

James Crowley EIT, RLS  
 (928) 203-5092  
[JCrowley@SedonaAZ.gov](mailto:JCrowley@SedonaAZ.gov)

**City Engineer:**

Kurt Harris, PE  
 (928) 203-5039  
[kharris@SedonaAZ.gov](mailto:kharris@SedonaAZ.gov)

**\$ FY24 Project Budget:** \$50,000  
**Total Project Budget:** \$1,575,600

The Transportation Master Plan, Strategy 11, Walking and Bicycling Facilities, indicates that these improvements collectively encourage use of alternative modes of travel in Sedona, and support a park-once culture where visitors and residents are encouraged to leave their vehicles at their place of lodging/residence. To have a measurable impact on traffic congestion, shared-use path connections will be required.

This project would provide a shared-use pathway connection from Navoti Drive to White Bear Road and Dry Creek Road. This will also provide a multimodal connection to western Sedona/Red Rock High School other than SR 89A.

Break out of Phase 1 includes portion of shared-use path from Dry Creek Road to back side of the Library in FY 2023. Remaining portion of the trail in Phase 2 is dependent upon easements from property owners and to be completed in FY 2024.

The construction contract with Standard Construction was approved by city council and the shared-use path is near completion. Access to the Sedona Public Library will remain open during the improvement project.

**Project Status**

**September 2023**

Project Phase I	% Completion	Completion Date
Design	100%	Summer 2022
Construction	100%	Summer 2023
