




City of Sedona Public Works Department

102 Roadrunner Drive Sedona, AZ 86336
(928) 204-7111 • Fax: (928) 282-5348

SD-12 - Schnebly & Grove Drainage Improvements

FY24 CIP Update

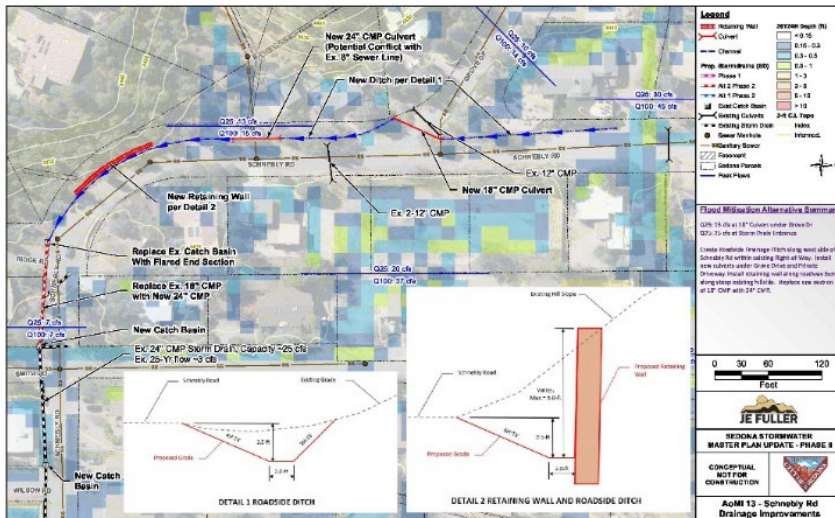

KEY FEATURES:

Consultant: JE Fuller

Contractor: TBD

Timing: FY23 Design; FY24 Construction

Construction Challenges:

- Limited right-of-way
- Maintain traffic flow
- Accommodate increased runoff due to build-out in the area

Project Manager:

Sandra Phillips, PE, CFM
(928) 203-0118
SPhillips@SedonaAZ.gov

City Engineer:

Kurt Harris, PE
(928) 203-5059
KHarris@SedonaAZ.gov

\$ FY24 Project Budget: \$313,100

Total Project Budget: \$626,200

Residents requested that the City review options to help alleviate drainage concerns in this area. Substantial flooding occurs in the area during monsoons. Infrastructure is well under capacity now that this area is built out.

Development of plans, specifications, and cost estimate to intercept and direct flows down Schnebly Road into existing infrastructure. This is a project created from the outreach to residents through the Stormwater Master Plan Update.

Consultant, JE Fuller, has been awarded the contract and completed 100% designs. The bid will be advertised in January, due in February, for an estimated construction start date in March 2024.

Project Status

January 2024

Project Phase

% Completion

Completion Date

Design

100%

December 2023

Construction

0%

Spring 2024
