




# City of Sedona Public Works Department

102 Roadrunner Drive Sedona, AZ 86336  
(928) 204-7111 • Fax: (928) 282-5348

## SD-12 - Schnebly & Grove Drainage Improvements

FY24 CIP Update

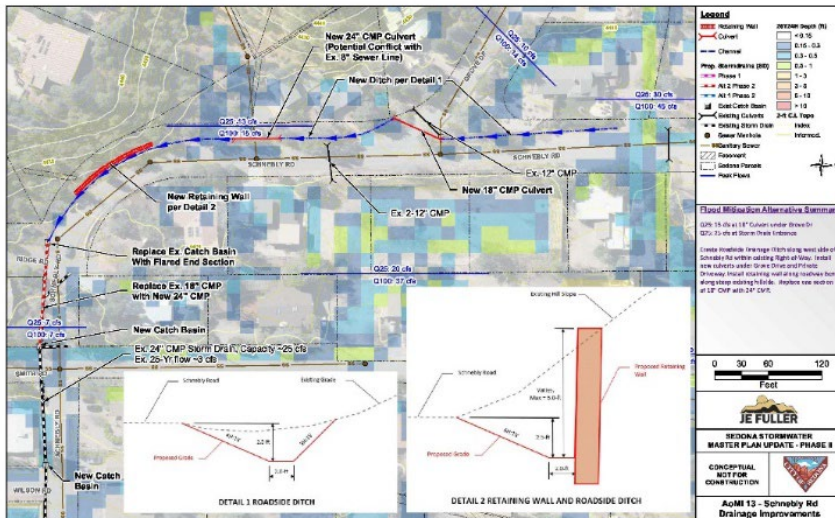

### KEY FEATURES:

- Consultant:** JE Fuller
- Contractor:** Asphalt Paving & Supply Inc.
- Timing:** FY23 Design; FY24 Construction
- Construction Challenges:**
  - Limited right-of-way
  - Maintain traffic flow
  - Accommodate increased runoff due to build-out in the area

### Project Manager:

Hanako Ueda, CFM  
(928) 203-5024  
[HUedas@SedonaAZ.gov](mailto:HUedas@SedonaAZ.gov)

### City Engineer:

Kurt Harris, PE  
(928) 203-5059  
[KHarris@SedonaAZ.gov](mailto:KHarris@SedonaAZ.gov)

**\$ FY24 Project Budget:** \$313,100  
**Total Project Budget:** \$626,200

Residents requested that the City review options to help alleviate drainage concerns in this area. Substantial flooding occurs in the area during monsoons. Infrastructure is well under capacity now that this area is built out.

Development of plans, specifications, and cost estimate to intercept and direct flows down Schnebly Road into existing infrastructure. This is a project created from the outreach to residents through the Stormwater Master Plan Update.

Consultant, JE Fuller, has been awarded the contract and completed 100% designs. Asphalt Paving & Supply Inc was awarded the construction contract and anticipate breaking ground in late March 2024.

### Project Status

March 2024

Project Phase	% Completion	Completion Date
Design	100%	December 2023
Construction	0%	Spring 2024
