




**City of Sedona**  
**Public Works Department**  
 102 Roadrunner Drive Sedona, AZ 86336  
 (928) 204-7111 • Fax: (928) 282-5348

**Sanborn Drive/Thunder Mountain Road Overlay** **FY18 CIP Update**

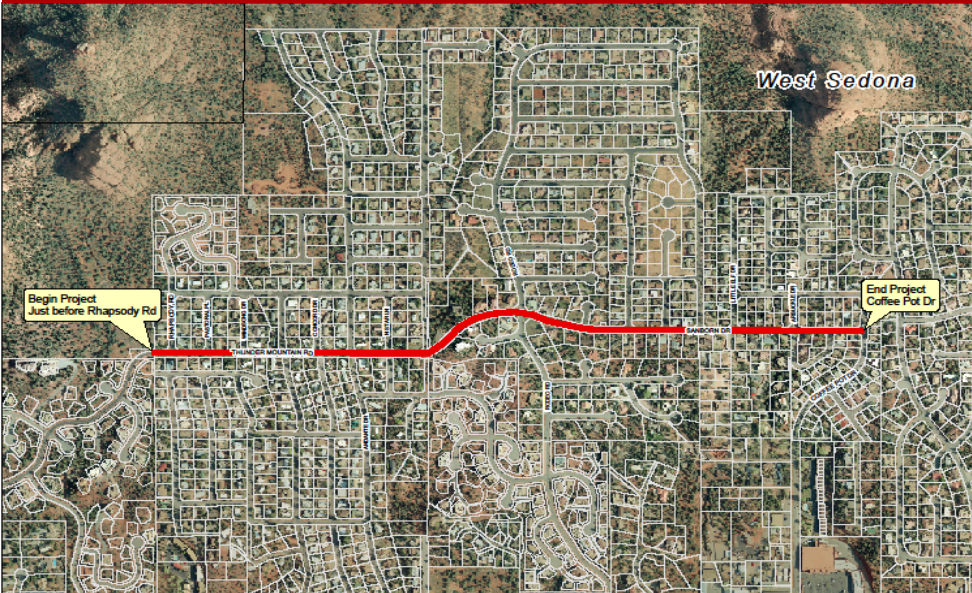

**KEY FEATURES:**

**Consultant:** Woodson Engineering, Inc.

**Contractor:** TBD

**Timing:** Fall 2018 Construction

**Construction Challenges:**

- Environmental Clearances
- Maintenance of Traffic

**Project Manager:**

Stephen Craver, PE  
 (928) 203-5059

[SCraver@SedonaAZ.gov](mailto:SCraver@SedonaAZ.gov)

**City Engineer:**

J. Andy Dickey, PE  
 (928) 203-5039

[ADickey@SedonaAZ.gov](mailto:ADickey@SedonaAZ.gov)

**\$ FY18 Project Budget:** \$75,750

**Total Project Budget:** \$682,174

The project will include a mill and overlay, with minor shoulder widening and curb along the south side of the roadway allowing for the construction of a shared use path in the future. The approximate one mile segment of Sanborn Drive/Thunder Mountain Road is between Rhapsody Road and Coffee Pot Drive.

This project is part of the Surface Transportation Program (STP), which is administered by the Northern Arizona Council of Governments (NACOG). A professional services contract with Woodson Engineering was approved by Council on September 13, 2016.

**Status:** Final plans, specifications, and cost estimate are expected in May 2018. A template IGA has been provided by ADOT and staff is compiling the documents necessary to establish the project in the HURF Exchange Program, which will eliminate the need to design and construct the roadway to federal standards, reducing overall costs in the process.

For a copy of this update, or updates for other projects, visit the projects website at: [www.sedonaaz.gov/CIP](http://www.sedonaaz.gov/CIP).

**Project Status** **March 2018**

Project Phase	% Completion	Completion Date
Design	95%	May 2018
Construction	0%	Fall 2018
