




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

Major Lift Station Upgrades - Design

FY21 CIP Update

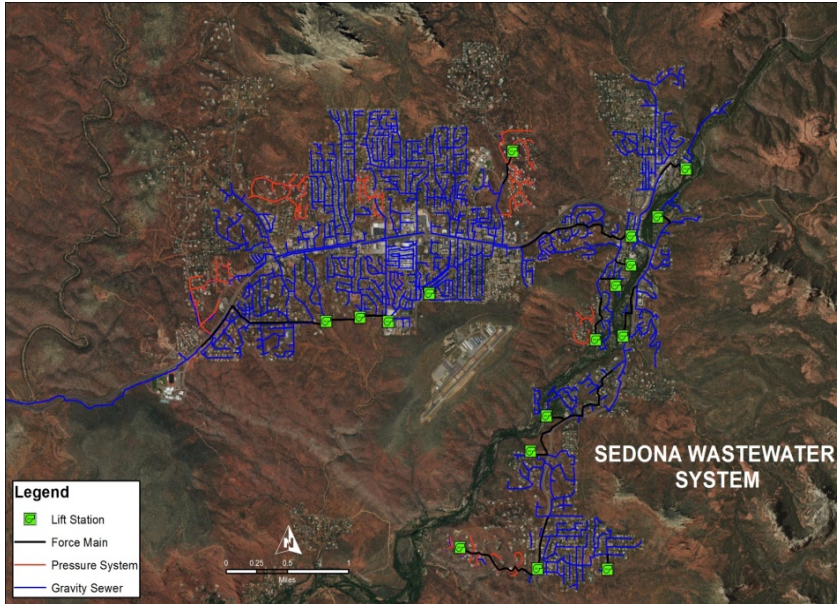

KEY FEATURES:

Consultant: Carollo Engineers, Inc.

Contractor: TBD

Timing: Spring 2021

Construction Challenges:

- Potential by-pass operations
- Maintaining operations of the lift stations

Project Manager:

Roxanne Holland, PE
 (928) 203-5069

RHolland@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039

ADickey@SedonaAZ.gov

\$ FY21 Project Budget: \$100,000
Total Project Budget: \$960,000

The Major Lift Station Upgrades project will make improvements at the three major lift stations; Brewer Rd., Carroll Canyon, and El Camino lift stations. Work will consist of upgrading obsolete controls, allowing for efficient and reliable automation. Additionally, coatings will be refreshed in the wet wells, and variable frequency drives, flow meters, and transfer switches will be replaced. Design of the upgrades will begin in Fiscal Year 2021, and construction is proposed in Fiscal Year 2022

Status: A Request for Qualifications (RFQ) to allow engineering firms to prepare proposals resulted in two firms submitting qualifications. Council approved award of a Design Services Contract with Carollo Engineers, Inc. for the design phase of this project. A kickoff meeting for design is scheduled in April 2021.

For a copy of this update, or updates for other projects, visit the projects website at: www.sedonaaz.gov/CIP.

Project Status **March 2021**

Project Phase	% Completion	Completion Date
Design	0%	Winter 2021
Construction	0%	Winter 2021/2022
