




City of Sedona Public Works Department

102 Roadrunner Drive Sedona, AZ 86336
(928) 204-7111 • Fax: (928) 282-5348



Sedona in Motion 4C – Pedestrian Crossing at Oak Creek

FY21 CIP Update

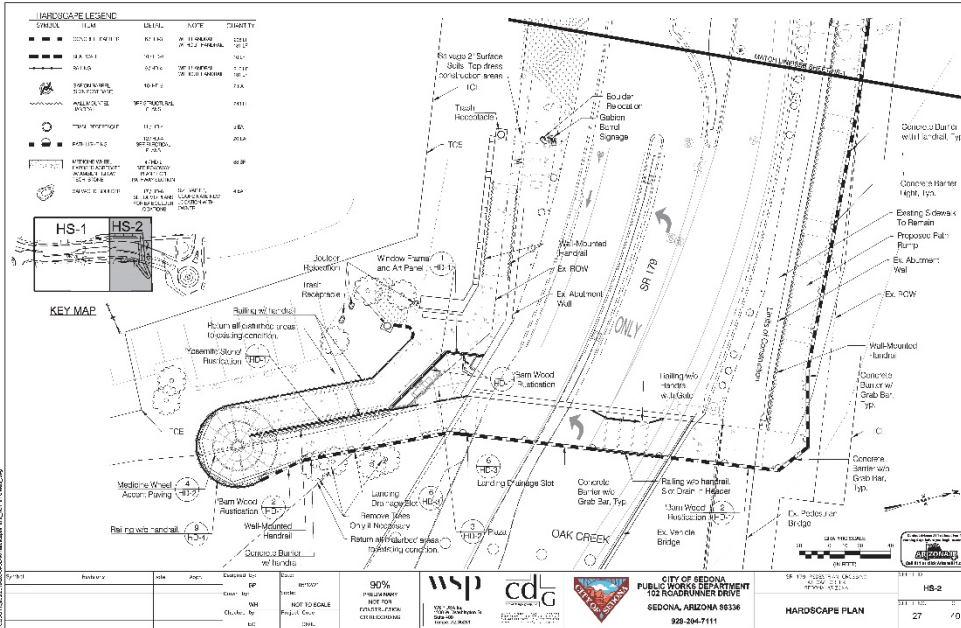

KEY FEATURES:

Consultant: JE Fuller/WSP

Contractor: TBD

Timing: FY 2018 – FY 2024

Construction Challenges:

- Heavy vehicular and pedestrian traffic
- Tight Construction Area
- Land acquisition
- Potential for restricted work hours
- Floodplain
- Property impacts
- Utility impacts

Project Manager:

Robert Welch, PE
(928) 203-5120

BWelch@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
(928) 203-5039

ADickey@SedonaAZ.gov

\$ FY20 Project Budget: \$252,500

Total Project Budget: \$2,261,100

This project is one of the transportation projects identified in the Transportation Master Plan and by Council as a priority. The project proposes construction of a pedestrian bridge, tunnel, or other pedestrian crossing of State Route 179 between Oak Creek and SR 89A. A Feasibility Study was recently completed for the crossing which identified alternatives and provided a recommendation for a crossing type.

Status: Project design and review has progressed from scoping to a 90% design development stage. Revised 90% progress plans are in process for resubmittal following concerns and potential impacts of the project on adjoining property. The proposed plan revision will consist of a re-alignment and redesign of the southern segment of the pathway. The re-design is anticipated to be completed by May.

The overall schedule for completion of design and permitting has been modified to 14 months. Staff and WSP will be coordinating the design with the State (ADOT) and Federal agencies, as well as local stakeholders, to develop comprehensive plans and specifications for the construction.

For a copy of this update, or updates for other projects, visit the projects website at: www.sedonaaz.gov/CIP.

Project Status

April 2021

Project Phase

% Completion

Completion Date

Design

90%

August 2021

Construction

0%

Spring/Summer 2022
