




Sedona in Motion 4C – Pedestrian Crossing at Oak Creek

FY22 CIP Update

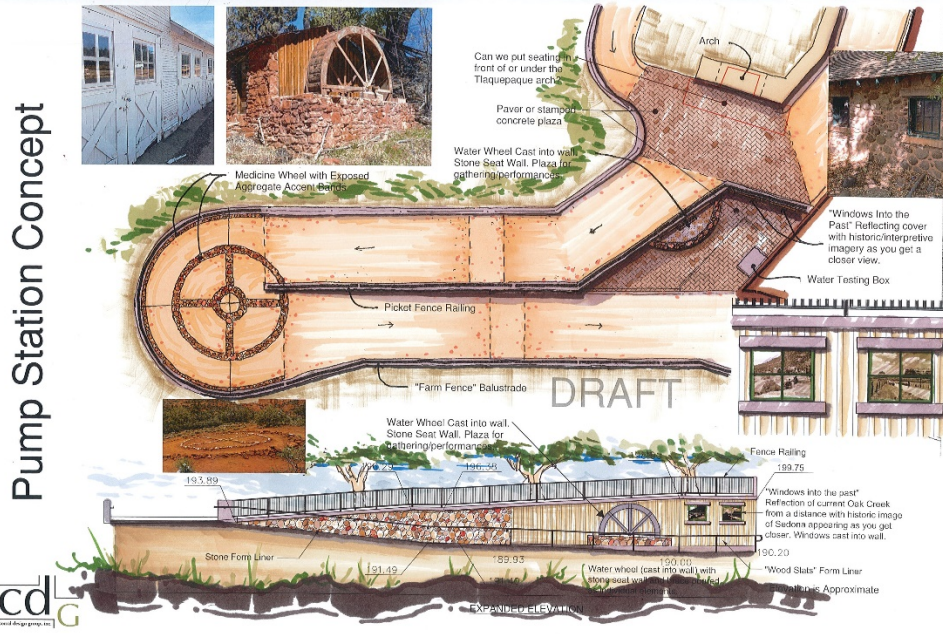

KEY FEATURES:

Consultant: JE Fuller/WSP

Contractor: TBD

Timing: FY 2018 – FY 2024

Construction Challenges:

- Heavy vehicular and pedestrian traffic
- Tight Construction Area
- Land acquisition
- Potential for restricted work hours
- Floodplain
- Property impacts
- Utility impacts

Project Manager:

Robert Welch, PE
 (928) 203-5120

BWelch@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039

ADickey@SedonaAZ.gov

\$ FY22 Project Budget: \$1,347,000

Total Project Budget: \$2,223,000

This project is one of the transportation projects identified in the Transportation Master Plan and by Council as a priority. The project proposes construction of a pedestrian bridge, tunnel, or other pedestrian crossing of State Route 179 between Oak Creek and SR 89A. A Feasibility Study was recently completed for the crossing which identified alternatives and provided a recommendation for a crossing type.

Status: Revised 90% progress plans incorporating at-grade crossing modifications were recently completed by the consultant. These revised plans are currently under review by staff and ADOT for permit review. The added design and resubmittal, including additional utility coordination and ADOT review/reapplication, has extended the project schedule approximately 3 additional months.

The overall schedule for completion of design and permitting has been modified to 14 months. Staff and WSP will be coordinating the design with the State (ADOT) and Federal agencies, as well as local stakeholders.

For a copy of this update, or updates for other projects, visit the projects website at: www.sedonaaz.gov/CIP.

Project Status

August 2021

Project Phase	% Completion	Completion Date
Design	90%	November/December 2021
Construction	0%	Spring/Summer 2022
