




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348



Sedona in Motion 8 – Enhanced Transit Service

FY22 CIP Update

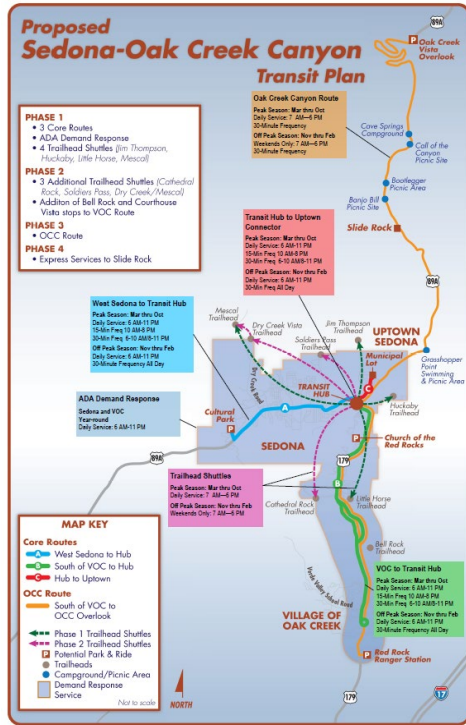

KEY FEATURES:

Consultant: LSC Transportation Consultants, Inc.

Contractor: TBD

Timing: July 2018 – FY 20

Construction Challenges:

- Bus stop locations
- Park and ride lot locations

Transit Administrator:

Robert Weber
 (928) 203-5086
RWeber@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039
ADickey@SedonaAZ.gov

This project consists of providing enhanced transit from the Village of Oak Creek, continuing north on SR 179 and SR 89A into Oak Creek Canyon. It includes periodic stops, park and ride lots, and trailhead service. Planning for the project includes representatives from City staff, ADOT, US Forest Service, AZ State Parks, Coconino County, Verde Lynx, Sedona Fire District, and the Sedona Chamber of Commerce. The first step will be implementation of Phase 1, which extends the core routes and includes a service to specific trailheads.

Status: At the May 11, 2021 Council meeting Council directed staff to proceed with the trailhead shuttle and microtransit plan as presented, to look at additional parking opportunities, and to evaluate the carbon offset of gasoline versus hybrid vehicles. Staff was also directed to proceed with steps required to permanently extend the transportation sales tax to fund implementation of the transit system. At the August 10 meeting, staff will be requesting approval to lease purchase five trailhead shuttle transit vehicles.

For more information on this project, visit the project website at: www.sedonaaz.gov/Transit.

\$ FY22 Project Budget: \$ 2,170,000
Total Project Budget: \$44,380,000

Project Status		August 2021	
Project Phase	% Completion	Completion Date	
Design	100%	October 2019	
Construction	0%	TBD	
