



SR179 Sewer Main Replacement: Phase 2

January 28, 2022

Welcome to the City of Sedona SR179 Sewer Main Replacement: Phase 2 eNews. Businesses and residents are reminded to call the **Project Hotline at (928) 852-4164** to speak to a project team member with any questions or concerns. Please note that in the event of inclement weather the work schedule may be altered or suspended without notice.

Sewer work is scheduled to be complete by the end of February, with final paving happening later in the spring when temperatures allow.

The City of Sedona and their contractor, Standard Construction Company, are working on the second, and final, phase of the SR179 Sewer Main Replacement Project. The project consists of the removal and replacement of approximately 365 feet of sewer main along SR179, from the stopping point of Phase 1 through the Schnebly Hill Roundabout. In addition to this work, approximately 400 feet of sewer main will be upgraded under the pedestrian bridge crossing Oak Creek adjacent to SR179.

SEWER MAIN INSTALLATION ONGOING

Crews will continue installing and connecting new sewer main along the east side of SR179, as highlighted in the map below. In addition to this work, crews will be potholing for utilities in the sidewalk in advance of sewer work across from Tlaquepaque. Work will occur in both the daytime and the nighttime.

Please be aware of the following impacts:

Monday, January 31 through Thursday, February 3, 7 a.m. – 5:30 p.m.

Please be aware of lane and sidewalk closures, rough road conditions, flagging operations, reduced speeds, and construction equipment along the project corridor. Access to businesses and residents will be provided at all times, however, temporary driveway closures will be necessary. The contractor will coordinate with local businesses to ensure access is continuously provided.

Sunday, January 30, Tuesday, February 1, and Wednesday, February 2, 10 p.m. – 7 a.m.

To minimize impacts to local businesses and the traveling public, night work will be necessary to complete this work. A pilot car operation will be in place to keep traffic moving despite full lane closures. Please allow for extra time to get through the area and follow all marked signage.

The City is dedicated to keeping residents, businesses, and visitors informed of potential impacts throughout the project.

Both the City and contractor would like to assure the local community that precautionary measures are in place to prevent impacts to Oak Creek, and to minimize impacts to local businesses and the traveling public.

Night work will be scheduled and is necessary to complete a portion of this project. A pilot car operation will be in place during night work to keep traffic moving, despite lane closures. Please allow for extra time to get through this area and follow all marked signage.


To speak to a project representative, call the **Project Hotline at (928) 852-4164**. For additional project information, scan the QR Code to the right.



STANDARD
CONSTRUCTION COMPANY, INC.
CIVIL GENERAL CONTRACTOR



SUNRISE
ENGINEERING

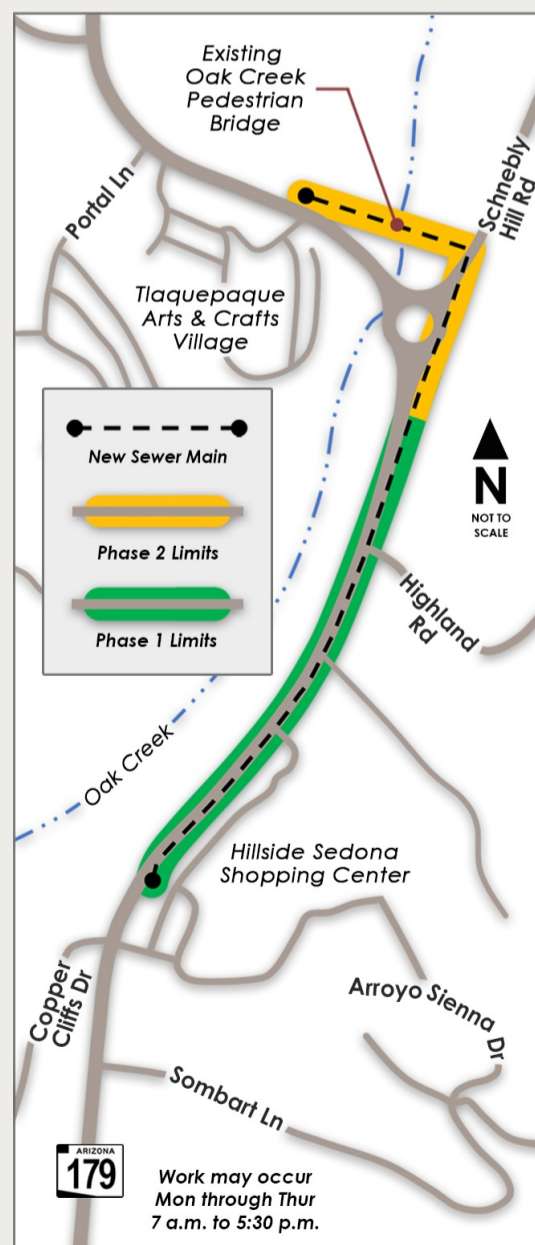

Work may occur
Mon through Thur
7 a.m. to 5:30 p.m.

To receive eNews project updates, email a request to:
news@sr179sewermainreplacement.com
