




**Sedona in Motion 4C – Pedestrian Crossing at Oak Creek**

**FY22 CIP Update**

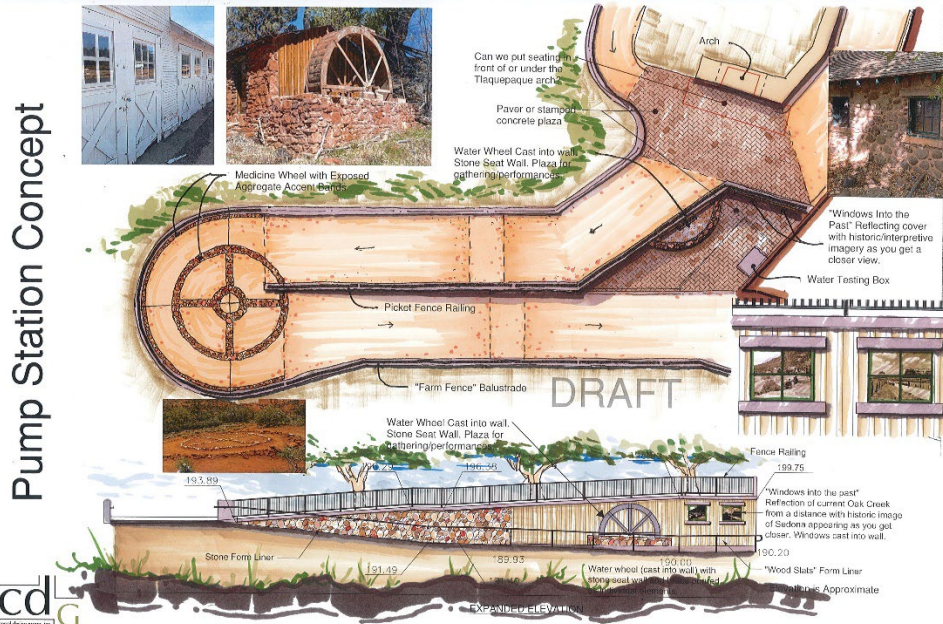

**KEY FEATURES:**

**Consultant:** JE Fuller/WSP

**Contractor:** TBD

**Timing:** FY 2018 – FY 2024

**Construction Challenges:**

- Heavy vehicular and pedestrian traffic
- Tight Construction Area
- Land acquisition
- Potential for restricted work hours
- Floodplain
- Property impacts
- Utility impacts

**Project Manager:**

Robert Welch, PE  
 (928) 203-5120

[BWelch@SedonaAZ.gov](mailto:RWelch@SedonaAZ.gov)

**City Engineer:**

J. Andy Dickey, PE  
 (928) 203-5039

[ADickey@SedonaAZ.gov](mailto:ADickey@SedonaAZ.gov)

**\$ FY22 Project Budget:** \$1,347,000

**Total Project Budget:** \$2,223,000

This project is one of the transportation projects identified in the Transportation Master Plan and by Council as a priority. The project proposes construction of a pedestrian bridge, tunnel, or other pedestrian crossing of State Route 179 between Oak Creek and SR 89A. A Feasibility Study was recently completed for the crossing which identified alternatives and provided a recommendation for a crossing type.

**Status:** 100% construction plans incorporating at-grade and grade separated crossing modifications were completed by the consultant. These plans remain under review by ADOT. Staff is continuing to coordinate with ADOT for permitting of the project.

The overall schedule for completion of design and permitting has been modified to 16 months. Construction of the project is anticipated to take 9 months. Staff and the Engineer (WSP) will be coordinating the construction with the State (ADOT) and Federal agencies, as well as local stakeholders.

For a copy of this update, or updates for other projects, visit the projects website at: [www.sedonaaz.gov/CIP](http://www.sedonaaz.gov/CIP).

**Project Status**

**April 2022**

Project Phase	% Completion	Completion Date
Design	98%	Summer 2022
Construction	0%	Fall/Winter 2022
