




**City of Sedona**  
**Public Works Department**  
 102 Roadrunner Drive Sedona, AZ 86336  
 (928) 204-7111 • Fax: (928) 282-5348

**WW-01D - WW Collection System Improvements**

**FY23 CIP Update**

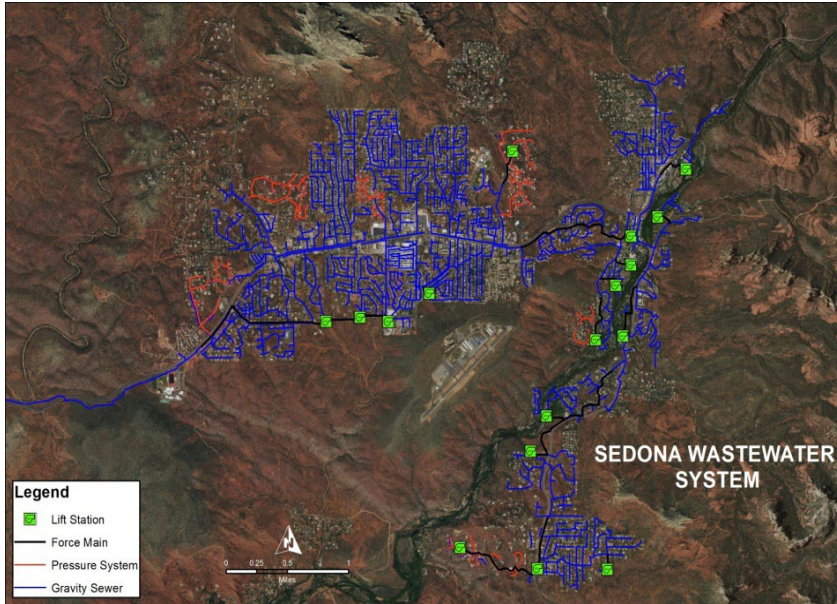

**KEY FEATURES:**

**Consultant:** TBD

**Contractor:** TBD

**Timing:** FY23

**Construction Challenges:**

- Potential by-pass operations
- Securing existing services
- Material availability

**Project Manager:**

Roxanne Holland, PE  
 (928) 203-5069

[RHolland@SedonaAZ.gov](mailto:RHolland@SedonaAZ.gov)

**City Engineer:**

J. Andy Dickey, PE  
 (928) 203-5039

[ADickey@SedonaAZ.gov](mailto:ADickey@SedonaAZ.gov)

**\$ FY23 Project Budget:** \$460,000  
**Total Project Budget:** \$460,000

The 2017 Wastewater Master Plan Update (WWMP) included both condition assessments of existing sewer infrastructure and capacity analysis of the sewer collection system. During the desktop condition assessment, several pipes were identified as having issues such as deteriorated pipe lining, offset joints, cracks in the pipe, and general deterioration from hydrogen sulfide gasses.

This project will install pipe lining in Foothills Drive and El Camino Road, replace a portion of the 18-inch main line in Northview Road, and repair offset joints and re-line the 8-inch mains in Lazy Bear Estates.

**Status:** Staff is currently negotiating with a design firm on a scope and fee for design services for the project. It is anticipated that construction will occur beginning in the spring of 2023.

**Project Status** **August 2022**

Project Phase	% Completion	Completion Date
Design	0%	Fall 2022
Construction	0%	Spring 2023
