




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348



Sedona in Motion 4C – Pedestrian Crossing at Oak Creek

FY23 CIP Update

Pump Station Concept

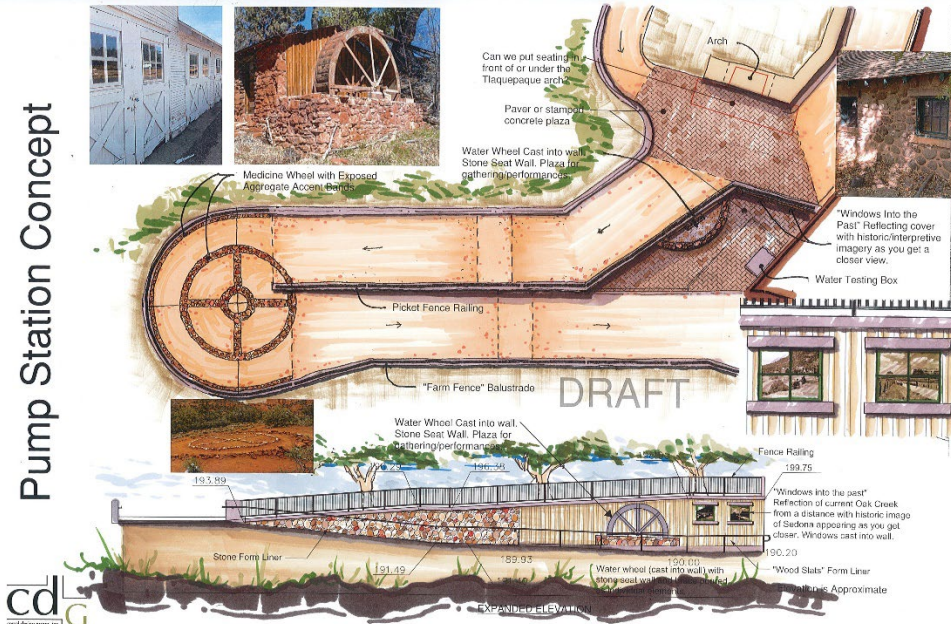

KEY FEATURES:

Consultant: JE Fuller/WSP

Contractor: TBD

Timing: FY 2018 – FY 2024

Construction Challenges:

- Heavy vehicular and pedestrian traffic
- Tight Construction Area
- Land acquisition
- Potential for restricted work hours
- Floodplain
- Property impacts
- Utility impacts

Project Manager:

Robert Welch, PE
 (928) 203-5120
BWelch@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039
ADickey@SedonaAZ.gov

\$ FY23 Project Budget: \$1,691,280
Total Project Budget: \$2,577,545

This project is one of the transportation projects identified in the Transportation Master Plan and by Council as a priority. The project proposes construction of a pedestrian bridge, tunnel, or other pedestrian crossing of State Route 179 between Oak Creek and SR 89A. A Feasibility Study was recently completed for the crossing which identified alternatives and provided a recommendation for a crossing type.

Status: 100% construction plans incorporating at-grade and grade separated crossing modifications were completed by the consultant. ADOT concluded its review of plans and final modifications to the plans are being made by the consultant. The project has been released for construction bidding with the bid solicitation scheduled to close on December 6 at 2:30 pm.

Construction of the project is anticipated to take 9 months. Staff and the Engineer (WSP) will be coordinating the construction with the State (ADOT) and Federal agencies, as well as local stakeholders.

Project Status

October 2022

Project Phase	% Completion	Completion Date
Design	98%	Summer 2022
Construction	0%	Fall/Winter 2023
