




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348



Sedona in Motion 5D – Brewer-Ranger Intersection

FY23 CIP Update

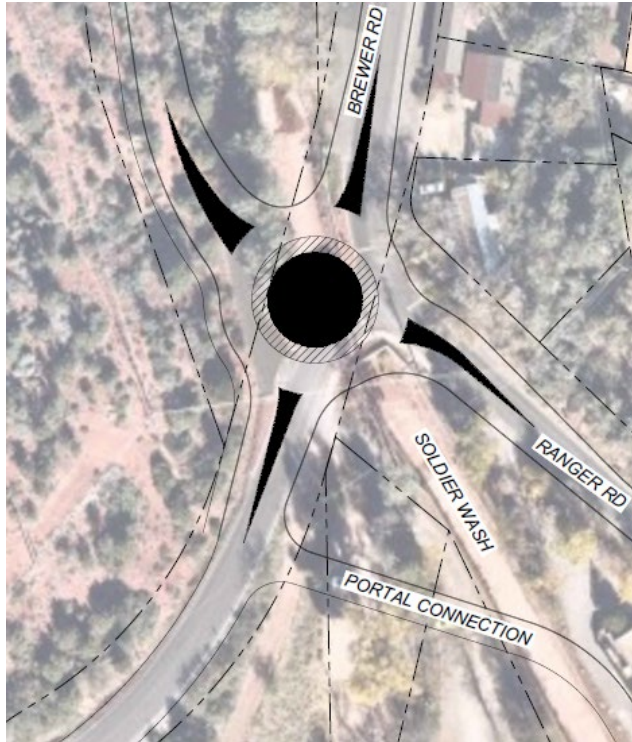

KEY FEATURES:

Consultant: Kimley-Horn

Contractor: TBD

Timing: January 2022 – June 2023

Construction Challenges:

- Adjacent driveways
- Limited footprint
- Proximity to Soldier Wash
- Public access to Brewer Road

Project Manager:

Kurtis Harris, PE
 (928) 203-5059
KHarris@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039
ADickey@SedonaAZ.gov

\$ FY23 Project Budget: \$2,810,000
Total Project Budget: \$2,949,300

This project has been identified as a need for many years but is now being prioritized based on the necessity of transit to utilize the intersection for access to the proposed transit hub location. The new intersection will include constructing a portion of a Ranger Road extension and will also look to accommodate the connection from Portal Lane to Brewer Road as part of SIM-5A. A design contract with Kimley-Horn was approved by Council on December 14, 2021. A project kick-off was held in early February.

Status: A public outreach meeting with Brewer Road residents and businesses was held on April 5. The 4-legged roundabout pictured above as the preferred alternative. Work on the final design has started and should be completed by fall 2022.

Project Status

October 2022

Project Phase	% Completion	Completion Date
Design	50%	October 2022
Construction	0%	June 2023
