




Sedona in Motion 4C – Pedestrian Crossing at Oak Creek

FY23 CIP Update

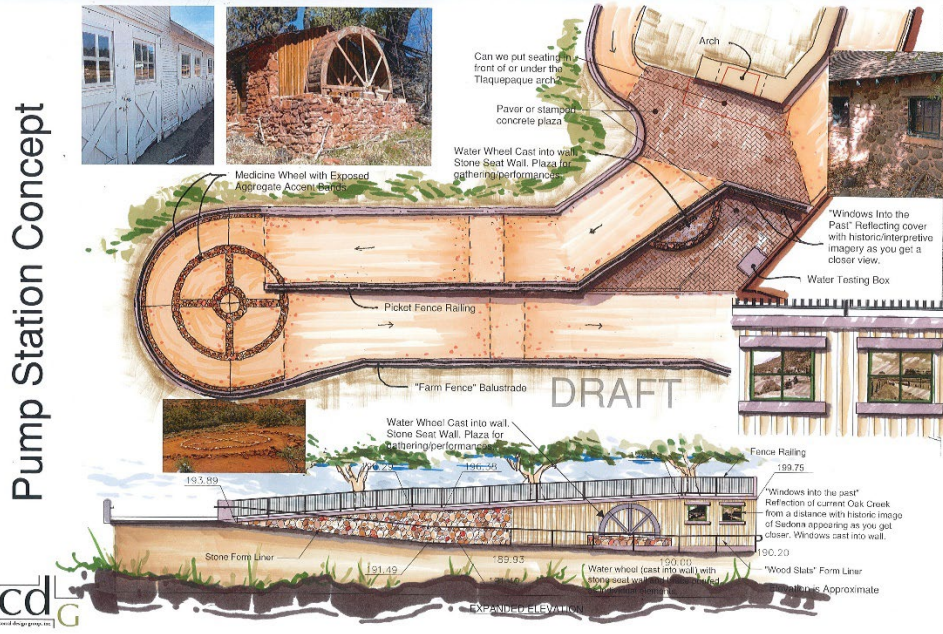

KEY FEATURES:

Consultant: JE Fuller/WSP

Contractor: TBD

Timing: FY 2018 – FY 2024

Construction Challenges:

- Heavy vehicular and pedestrian traffic
- Tight Construction Area
- Land acquisition
- Potential for restricted work hours
- Floodplain
- Property impacts
- Utility impacts

Project Manager:

Robert Welch, PE
 (928) 203-5120
BWelch@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039
ADickey@SedonaAZ.gov

\$ FY23 Project Budget: \$1,691,280
Total Project Budget: \$2,577,545

This project is one of the transportation projects identified in the Transportation Master Plan and by Council as a priority. The project proposes construction of a pedestrian bridge, tunnel, or other pedestrian crossing of State Route 179 between Oak Creek and SR 89A. A Feasibility Study was completed for the crossing which identified alternatives and provided a recommendation for a crossing type.

Status: 100% construction plans incorporating at-grade and grade separated crossing modifications were completed by the consultant. ADOT concluded its review of plans and final modifications to the plans are being made by the consultant. Following disappointing results from a recent bid solicitation, plans and specifications were revised and a second bid solicitation was let and is anticipated to close on March 23, 2023.

Once initiated, construction of the project is anticipated to take 9 months. Staff and the Engineer (WSP) will be coordinating the construction with the State (ADOT) and Federal agencies, as well as local stakeholders.

Project Status **February 2023**

Project Phase	% Completion	Completion Date
Design	100%	Fall 2022
Construction	0%	Spring 2024
