




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348



Sedona in Motion 5D – Brewer-Ranger Intersection

FY23 CIP Update

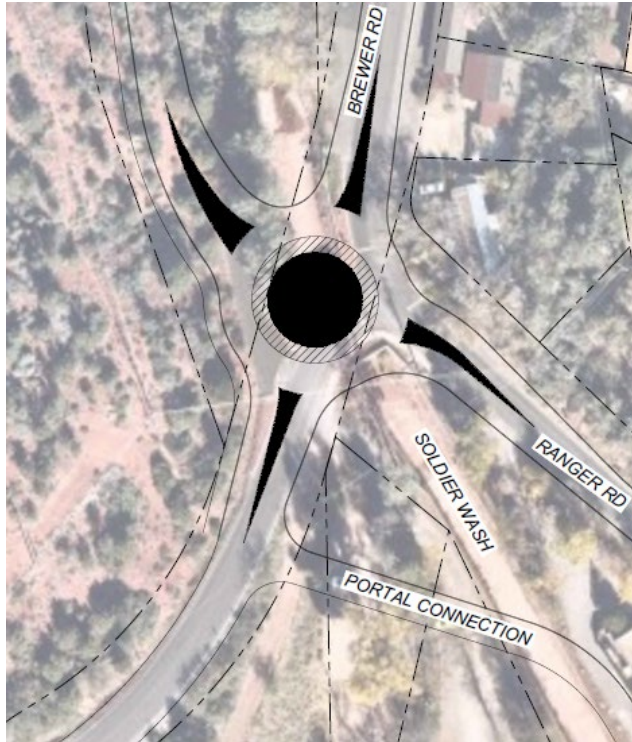

KEY FEATURES:

Consultant: Kimley-Horn

Contractor: TBD

Timing: January 2022 – January 2024

Construction Challenges:

- Adjacent driveways
- Limited footprint
- Proximity to Soldier Wash
- Public access to Brewer Road

Project Manager:

Kurtis Harris, PE
 (928) 203-5059
KHarris@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039
ADickey@SedonaAZ.gov

\$ FY23 Project Budget: \$90,130
Total Project Budget: \$2,341,770

This project has been identified as a need for many years but is now being prioritized based on the necessity of transit to utilize the intersection for access to the proposed transit hub location. The new intersection will include constructing a portion of a Ranger Road extension and will also look to accommodate the connection from Portal Lane to Brewer Road as part of SIM-5A. A design contract with Kimley-Horn was approved by Council on December 14, 2021. A project kick-off was held in early February.

Status:

60% design completion as of December 2022. Seismic and borings subsurface assessment complete for the retaining walls for Shared Used Path (SUP) value engineering evaluation. Soldier Wash FEMA flood modeling has demonstrated NO rise to floodplain negating further complicating design and permitting coordination with both Yavapai and Navajo County. Portal to Brewer Road design is being coordinated by Ardurra Engineering. Work on the final design has started and should be completed by late winter 2023.

Project Status

April 2023

Project Phase	% Completion	Completion Date
Design	90%	June 2023
Construction	0%	June 2024
