




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

Sedona in Motion 11N - Harmony SUP & Drainage Improvements

FY23 CIP Update

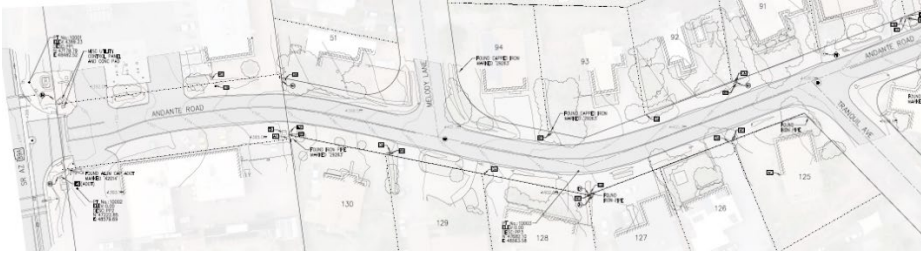

KEY FEATURES:

Consultant: Paradigm

Contractor: TBD

Timing: FY23/FY25

Construction Challenges:

- Limited right-of-way
- Ditches and driveways on both sides
- Lots drain to ditches

Project Manager:

Sandra Phillips, PE, CFM
 (928) 203-5076

SPhillips@SedonaAZ.gov

City Engineer:

Kurt Harris, PE
 (928) 203-5039

kharris@SedonaAZ.gov

\$ FY23 Project Budget: \$155,000

Total Project Budget: \$1,369,000

The residents of this neighborhood have requested sidewalks and paths for safe pedestrian travel. The Council discussed this project at the retreat as an important project to continue to move ahead as a priority.

Community Outreach meeting occurred in December, 2022 at the Sedona Public Library on White Bear Road. Different options were presented to the attendees/residents and participants were asked to identify their preferred option. Bi-lingual door hangers were placed to notify residents of the outreach meeting as well as a letter sent out. Results of outreach showed Andante as the preferred location of the SUP. Consultant was hired to gather topographic information and evaluate whether the east or west side would be best for the path placement. Speed tables will also be evaluated. Unfortunately the Federal RAISE Grant application was not accepted.

This project would provide a shared-use pathway connection from Thunder Mountain Road to SR 89A. This will also provide a multimodal connection to businesses for the residents of this neighborhood.

Project Status

June 2023

Project Phase	% Completion	Completion Date
Feasibility	30%	FY24
Design	0%	TBD
Construction	0%	TBD
