




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348



Sedona in Motion 4C – Pedestrian Crossing at Oak Creek

FY24 CIP Update

Pump Station Concept

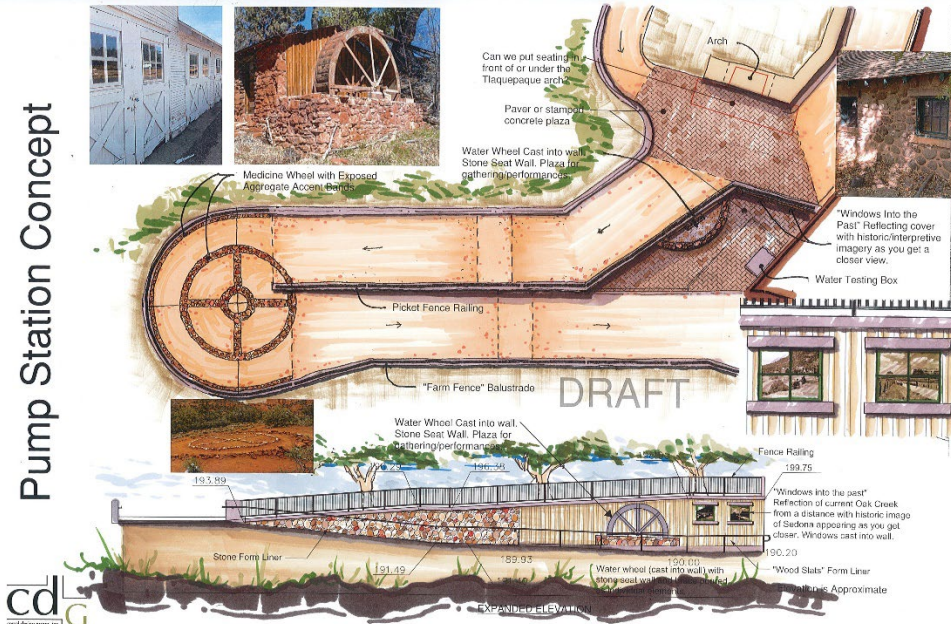

KEY FEATURES:

Consultant: JE Fuller/WSP

Contractor: TBD

Timing: FY 2018 – FY 2024

Construction Challenges:

- Heavy vehicular and pedestrian traffic
- Tight Construction Area
- Land acquisition
- Potential for restricted work hours
- Floodplain
- Property impacts
- Utility impacts

Project Manager:

Robert Welch, PE
 (928) 203-5120
BWelch@SedonaAZ.gov

City Engineer:

Kurt Harris, PE
 (928) 203-5059
KHarris@SedonaAZ.gov

\$ FY24 Project Budget: \$3,517,000
Total Project Budget: \$5,167,800

This project is one of the transportation projects identified in the Transportation Master Plan and by Council as a priority. The project proposes construction of a pedestrian bridge, tunnel, or other pedestrian crossing of State Route 179 between Oak Creek and SR 89A. A Feasibility Study was completed for the crossing which identified alternatives and provided a recommendation for a crossing type.

Status: The project is currently under construction by J. Banicki Construction, Inc. Work thus far has focused on the demolition and removal of existing infrastructure (walls, Archway, and gabions), relocation of utilities, development of construction access, and installation of measures to protect existing trees. City of Sedona is pleased to be working with the Banicki Construction. It is anticipated that the construction will take approximately 9 months to complete.

City staff, ADOT and the consultant (WSP) will be coordinating oversight of the construction with County and Federal agencies, as well as local stakeholders.

The City of Sedona will be working on a public outreach program to keep residents and businesses informed on the construction as well as a project hotline for questions and concerns.

Project Status

September 2023

Project Phase	% Completion	Completion Date
Design	100%	Fall 2022
Construction	0%	Spring 2024
