




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

WW-01D - WW Collection System Improvements

FY24 CIP Update

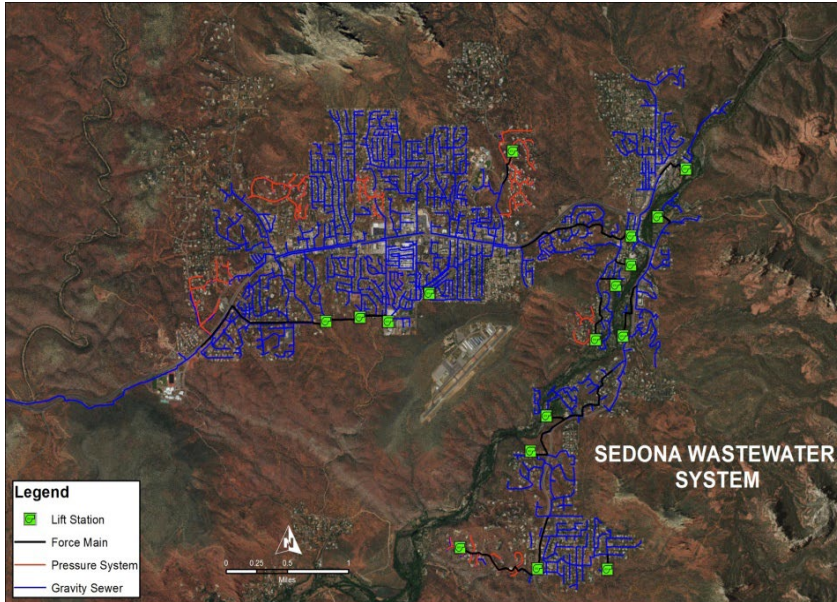

KEY FEATURES:

Consultant: ADC Wastewater Engineering

Contractor: TBD

Timing: FY24- FY25

Construction Challenges:

- Potential by-pass operations
- Securing existing services
- Material availability

Project Manager:

Roxanne Holland, PE
 (928) 203-5069

RHolland@SedonaAZ.gov

City Engineer:

Kurtis Harris, PE
 (928) 203-5059

KHarris@SedonaAZ.gov

\$ FY24 Project Budget: \$240,000

Total Project Budget: \$460,000

The 2017 Wastewater Master Plan Update (WWMP) included both condition assessments of existing sewer infrastructure and capacity analysis of the sewer collection system. During the desktop condition assessment, several pipes were identified as having issues such as deteriorated pipe lining, offset joints, cracks in the pipe, and general deterioration from hydrogen sulfide gasses.

This project will install pipe lining in Foothills Drive and El Camino Road, replace a portion of the 6-inch main line in Northview Road, and repair offset joints and re-line the 8-inch mains in Lazy Bear Estates.

Status: Design for the Northview Road sewer replacement is 90% complete, construction is anticipated to begin in Spring 2024. Design for Foothills Drive, El Camino Road, and Lazy Bear estates is anticipated to begin in February 2024.

Project Status **January 2024**

Project Phase	% Completion	Completion Date
Design	50%	Winter 2024
Construction	0%	Fall 2024
