




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348



Sedona in Motion 8 – Enhanced Transit Service - Tourism

FY21 CIP Update

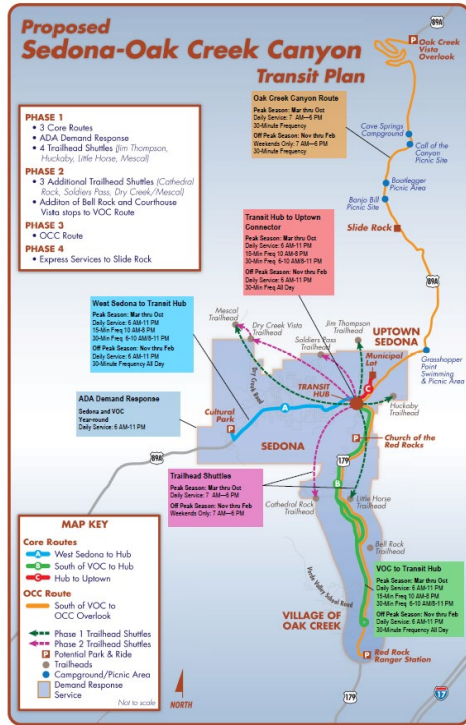

KEY FEATURES:

Consultant: LSC Transportation Consultants, Inc.

Contractor: TBD

Timing: July 2018 – FY 20

Construction Challenges:

- Bus stop locations
- Park and ride lot locations

Transit Administrator:

Robert Weber
 (928) 203-5086
RWeber@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039
ADickey@SedonaAZ.gov

This project consists of providing enhanced transit from the Village of Oak Creek, continuing north on SR 179 and SR 89A into Oak Creek Canyon. It includes periodic stops, park and ride lots, and trailhead service. Planning for the project includes representatives from City staff, ADOT, US Forest Service, AZ State Parks, Coconino County, Verde Lynx, Sedona Fire District, and the Sedona Chamber of Commerce. The first step will be implementation of Phase 1, which extends the core routes and includes a service to specific trailheads. The Transit Administrator position was recently filled by Robert Weber who is currently getting acquainted with his new position and becoming familiar with the details and matters associated with the proposed new transit system and center.

Status: Acceleration of the trailhead shuttle service, micro-transit services, and possible permanent extension of the 1/2 cent transportation sales tax will be discussed at the May 11, 2021 Council meeting.

For more information on this project, visit the project website at: www.sedonaaz.gov/Transit.

\$ FY21 Project Budget: \$1,670,000
Total Project Budget: \$59,935,000

Project Status

April 2021

Project Phase	% Completion	Completion Date
Design	100%	October 2019
Construction	0%	TBD
