




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

Brewer Road Force Main Valve Replacements

FY22 CIP Update

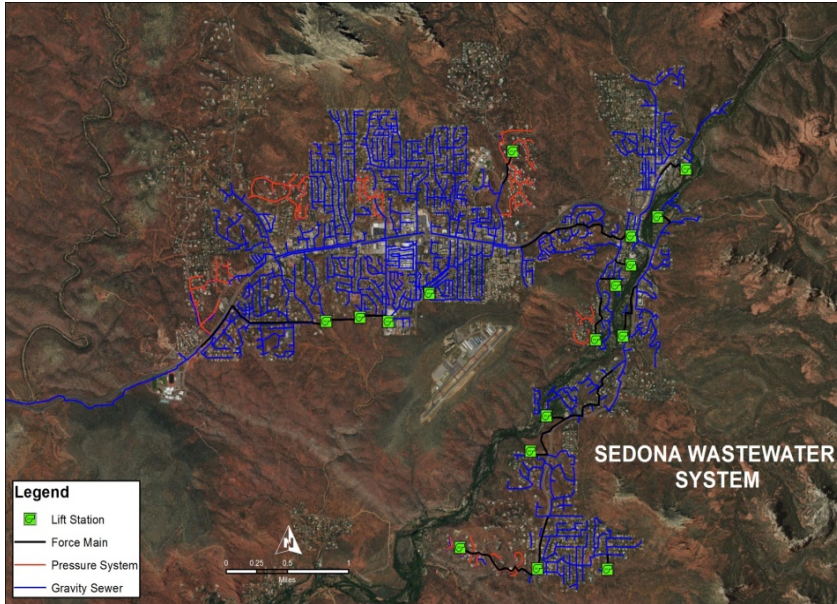

KEY FEATURES:

Consultant: N/A

Contractor: Construction Product Marketing

Timing: Fall 2021

Construction Challenges:

- Terrain
- Removal of old valves

Project Manager:

Roxanne Holland, PE
 (928) 203-5069

RHolland@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039

ADickey@SedonaAZ.gov

\$ FY22 Project Budget: \$100,000

Total Project Budget: \$100,000

The 2017 Wastewater Master Plan Update (WWMP) included condition assessments of existing sewer infrastructure. During the evaluations, it was determined that the Brewer Road Force Main air release/vacuum breaking valves should be replaced in order to maintain proper functionality of the force main. This project will replace the air release/vacuum breaking valves in the Brewer Road force main.

Status: Staff contracted with Construction Product Marketing for procurement and installation of the new valves. The initial testing of the existing valves is scheduled in October 2021.

For a copy of this update, or updates for other projects, visit the projects website at: www.sedonaaz.gov/CIP.

Project Status **September 2021**

Project Phase	% Completion	Completion Date
Design	n/a	n/a
Construction	0%	Fall 2021
