




Forest-Ranger-SR 89A Intersection

FY22 CIP Update

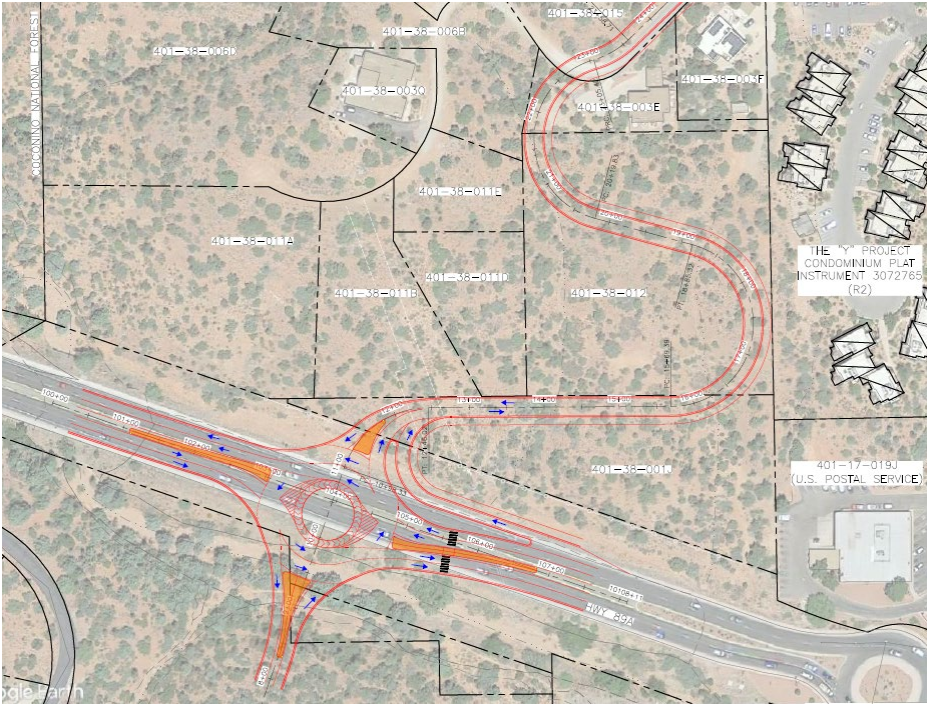

KEY FEATURES:

Consultant: Kimley-Horn

Contractor: TBD

Timing: January 2022 – June 2024

Construction Challenges:

- Adjacent grades
- Proximity to Soldier Wash
- Public access to Brewer Road

Project Manager:

Stephen Craver, PE
 (928) 203-5059

SCraver@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039

ADickey@SedonaAZ.gov

\$ FY22 Project Budget: \$67,000

Total Project Budget: \$2,949,300

This project was not initially included in the Transportation Master Plan. However, based on continued observation and the development of the Uptown Parking Garage and Transit Hub locations, staff believes an improved intersection at the new Forest extension and Ranger extension will provide congestion relief benefit. The image above is a concept of what a potential roundabout at the project location may look like. The project will also include a new bus lane on SR 89A and modifications to the Brewer Road roundabout.

Status: Kimley-Horn is under contract to complete a study to determine what the preferred intersection alternative will be. The study will also identify how the Brewer roundabout may be changed and will include additional traffic modeling to quantify expected congestion relief benefits from these and other downstream improvements for southbound SR 179 through the Schnebly Hill roundabout. The study is expected to kick off in May, now that the Brewer/Ranger intersection alternative has been finalized.

For a copy of this update, or updates for other projects, visit the projects website at: www.sedonaaz.gov/CIP.

Project Status

April 2022

Project Phase	% Completion	Completion Date
Study	0%	June 2022
Construction	0%	TBD
