




**City of Sedona**  
**Public Works Department**  
 102 Roadrunner Drive Sedona, AZ 86336  
 (928) 204-7111 • Fax: (928) 282-5348

**SD-03 - Back O' Beyond Low Water Crossing**

**FY23 CIP Update**

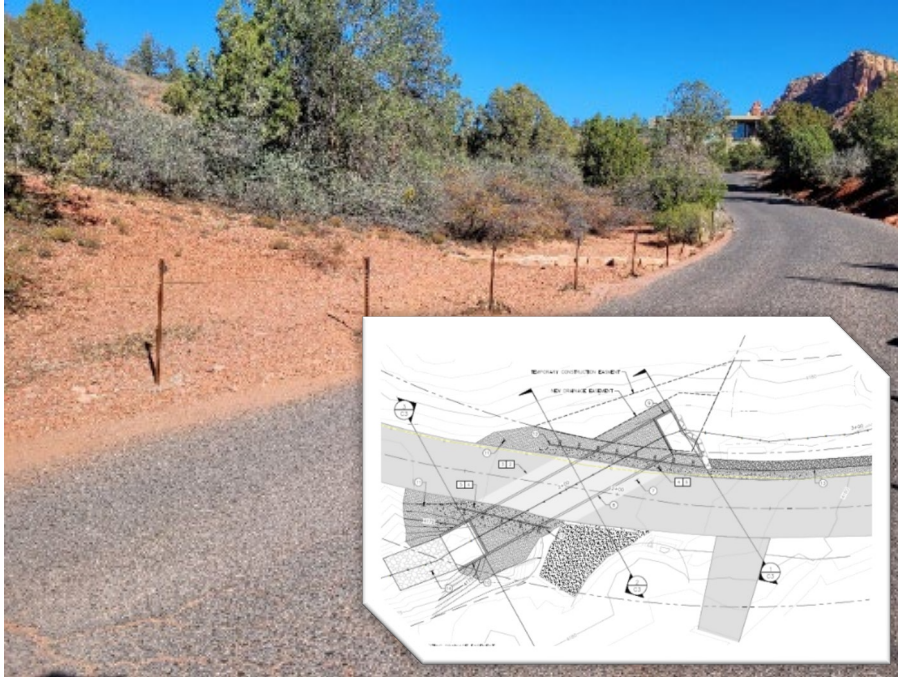

**KEY FEATURES:**

**Consultant:** Shephard-Wesnitzer, Inc.

**Contractor:** N/A

**Timing:**

Design: FY 2023

Construction: FY23

**Construction Challenges**

Narrow right-of-way

Necessity to keep a portion of roadway traversable.

**Project Manager:**

Johnathan Hoffman

(928) 203-5124

[JHoffman@SedonaAZ.gov](mailto:JHoffman@SedonaAZ.gov)

**City Engineer:**

J. Andy Dickey, PE

(928) 203-5039

[ADickey@SedonaAZ.gov](mailto:ADickey@SedonaAZ.gov)

**\$ FY23 Project Budget:** \$772,750

**Total Project Budget:** \$847,750

During significant storm events, the at-grade wash crossing of Back O' Beyond Road would be covered with water, isolating residents and visitors to the Cathedral Rock Trailhead.

This project will develop the design and costs to improve public road ingress and egress for the public in this area.

The 2005 Stormwater Master Plan did not identify this project. This project was escalated in priority due to public safety and cost of maintaining this crossing when rainfall events occurred. Excessive debris, soil and rock would need to be removed from this crossing.

Corps of Engineers' requirements will be determined, and right-of-way needs will be defined.

Project Update: A small portion of the project is on personal property. This required the City of Sedona to receive a permanent drainage easement. The easement process is complete. Shephard-Wesnitzer is finishing small design changes on the 90% plans requested by the City of Sedona. Bid advertisements will begin early next year.

**Project Status**

**December 2022**

Project Phase	% Completion	Completion Date
Design	90%	FY23
Construction	0%	FY23
