




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348



ST-08 - Forest-Ranger-SR 89A Intersection Improvements

FY23 CIP Update

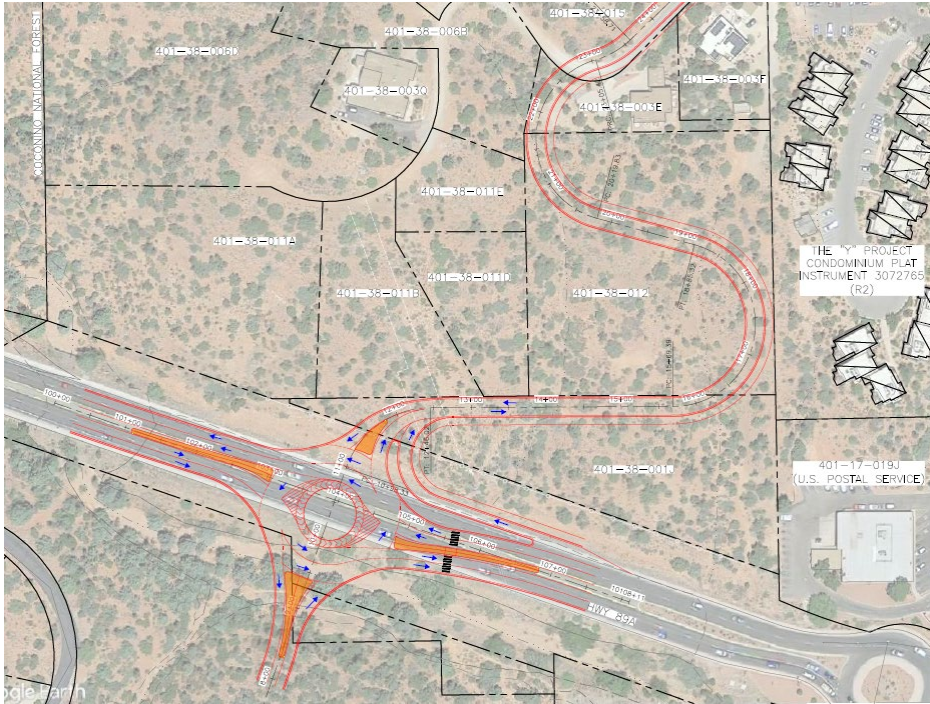

KEY FEATURES:

Consultant: Kimley-Horn

Contractor: TBD

Timing: January 2022 – June 2024

Construction Challenges:

- Adjacent grades
- FEMA floodplain associated with Soldier Wash transecting project
- Relocate overhead power lines to underground conduit
- Public access to Brewer Road

Project Manager:

Kurtis Harris, PE
 (928) 203-5059
KHarris@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039
ADickey@SedonaAZ.gov

\$ FY23 Project Budget: \$454,500
Total Project Budget: \$5,066,500

The City of Sedona's 2018 Transportation Master Plan identifies the Forest/Ranger/SR89a Intersection Improvement project as a key strategy to address the traffic congestion and improve overall regional connectivity. This project will reduce congestion during peak traffic from SR179 to 'Y' SR89a to Uptown Sedona (and further on to Flagstaff). This project will alleviate congestion, improve emergency access, promote multimodal travel (bus lane to HUB Exchange (working name), provide tourism management (by managing traffic congestion), improve workforce access to employment, and support local business sustainability.

Status: Kimley-Horn completed the study this month to determine what the preferred intersection alternative will be and include transit services. The study recommends an Urban Double Lane Roundabout to connect with the Brewer roundabout that will improve overall safety and efficiency. Traffic modeling quantified expected congestion relief benefits from these and other downstream improvements for southbound SR 179 through the Schnebly Hill roundabout.

Project Status

December 2022

Project Phase	% Completion	Completion Date
Study	100%	December 2022
Construction	0%	TBD
