




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348



ST-08 - Forest-Ranger-SR 89A Intersection Improvements

FY23 CIP Update

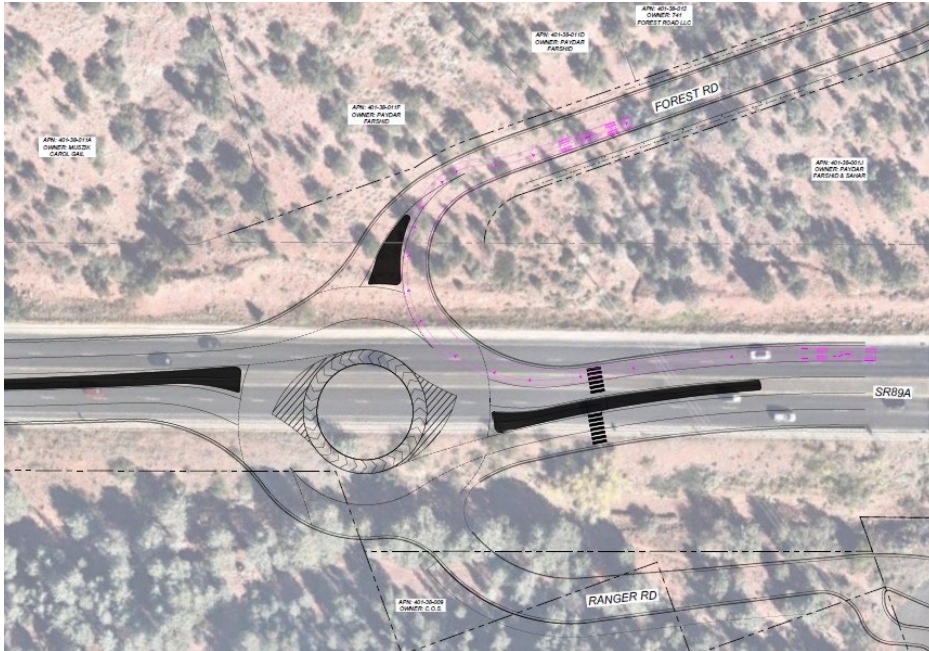

KEY FEATURES:

Consultant: Kimley-Horn

Contractor: TBD

Timing: January 2022 – June 2024

Construction Challenges:

- Adjacent grades
- FEMA floodplain associated with Soldier Wash transecting project
- Relocate overhead power lines to underground conduit
- Public access to Brewer Road
- Accommodating traffic

Project Manager:

Kurtis Harris, PE
 (928) 203-5059
KHarris@SedonaAZ.gov

City Engineer:

J. Andy Dickey, PE
 (928) 203-5039
ADickey@SedonaAZ.gov

\$ FY23 Project Budget: \$200,350
Total Project Budget: \$5,205,758

The City of Sedona's 2018 Transportation Master Plan identifies the Forest/Ranger/SR89a Intersection Improvement project as a key strategy to address the traffic congestion and improve overall regional connectivity. This project will reduce congestion during peak traffic from SR179 to 'Y' SR89a to Uptown Sedona (and further on to Flagstaff). This project will alleviate congestion, improve emergency access, promote multimodal travel (bus lane to HUB Exchange (working name), provide tourism management (by managing traffic congestion), improve workforce access to employment, and support local business sustainability.

Status: Kimley-Horn study recommends an Urban Double Lane Roundabout to connect with the Brewer roundabout that will improve overall safety and efficiency. Brewer Roundabout will be modified as an only right-in and right-out. Traffic modeling quantified expected congestion relief benefits from these and other downstream improvements for southbound SR 179 through the Schnebly Hill roundabout. Design cost approval is to go to council June 13th.

Project Status

April 2023

Project Phase	% Completion	Completion Date
Design	0%	December 2023
Construction	0%	TBD
