




**City of Sedona**  
**Public Works Department**  
 102 Roadrunner Drive Sedona, AZ 86336  
 (928) 204-7111 • Fax: (928) 282-5348

**PT-04B – North State Route 179 Park and Ride**

**FY23 CIP Update**

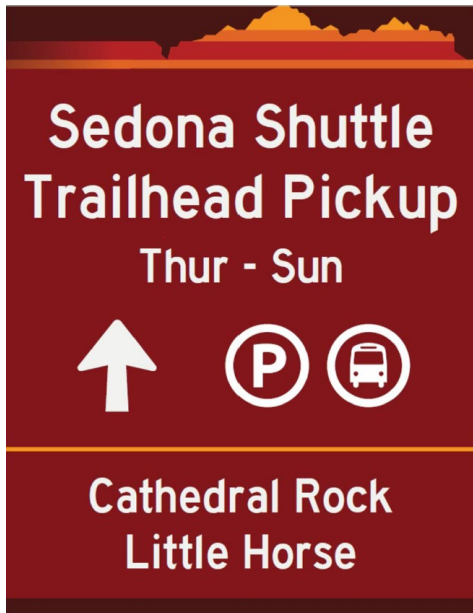

**KEY FEATURES:**

**Consultant:** Paradigm Design

**Contractor:** To be determined

**Timing:** FY23 to FY 25

**Design Challenges:**

- Possible improved connectivity To SR179
- Parking security and control

**Project Manager:**

John Hall, PE  
 (928) 203 – 5125  
[JHall@SedonaAZ.gov](mailto:JHall@SedonaAZ.gov)

**City Engineer:**

Kurtis Harris, P.E.  
 (928) 203-5039  
[KHarris@SedonaAZ.gov](mailto:KHarris@SedonaAZ.gov)

**\$ FY22/23 Project Budget:** \$2,000,000  
**Total Project Budget:** \$ 2,373,342

Traffic congestion during the peak visitor season continues to be the number one complaint by the residents of the City of Sedona. Add to that the overflow of trailhead parking into some of the city's neighborhoods and surface streets, and it becomes clear that this issue is adversely affecting public safety as well as the quality of life of residents and tourists alike.

To alleviate traffic congestion, the trailhead shuttle system was created and became operational in March of 2022. At the subject Park & Ride facility on Bowstring Drive, the leased parking lot was purchased from the Church of the Red Rocks in June of 2023. This will allow the City to make the necessary improvement for long term transit operations.

A conceptual design was completed last year for the proposed provision of permanent public restrooms, shade structures and other amenities to enhance the Sedona Shuttle experience.

Final design consultants have been selected to carry out the completion of design option analyses and the preparation of construction plans for an improved shuttle pickup facility.

**Project Status**

**June 2023**

Project Phase	% Completion	Completion Date
Final Design	0%	FY24
Construction	0%	FY25
