




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

PT-04B – North State Route 179 Park and Ride Improvements

FY24 CIP Update

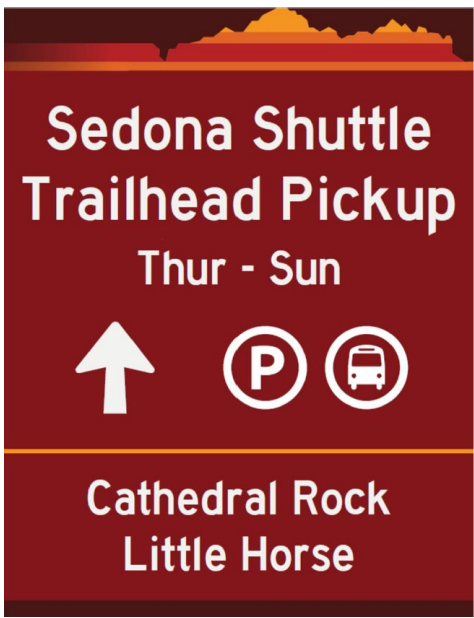

KEY FEATURES:

Consultant: Paradigm Design

Contractor: To be determined

Timing: FY23 to FY 25

Design Challenges:

- Possible improved connectivity To SR179
- Parking security and control

Project Manager:

John Hall, PE
 (928) 203 – 5125
JHall@SedonaAZ.gov

City Engineer:

Kurtis Harris, P.E.
 (928) 203-5039
KHarris@SedonaAZ.gov

\$ FY23 Land Budget: \$1,707,000
FY24 Design Budget: \$30,000
Total Project Budget: \$2,073,342

Traffic congestion during the peak visitor season continues to be the number one complaint by the residents of the City of Sedona. Add to that the overflow of trailhead parking into some of the City's neighborhoods and surface streets, and it becomes clear that this issue is adversely affecting public safety as well as the quality of life of residents and tourists. To alleviate traffic congestion, the trailhead shuttle system was created and became operational in March of 2022. At the subject Park & Ride facility on Bowstring Drive, the leased parking lot was purchased from the Church of the Red Rocks in June of 2023. This will allow the City to make the necessary improvements for long term transit operations.

A conceptual design was completed last year for the proposed provision of permanent public restrooms, shade structures and other amenities to enhance the Sedona Shuttle experience.

Final design is currently about 50 percent completed, with an early Encroachment Permit application being reviewed by ADOT, as a bus slip lane has been added to make a more direct connection to SR 179.

Project Status

November 2023

Project Phase	% Completion	Completion Date
Final Design	50%	FY24
Construction	0%	FY25
