




**City of Sedona**  
**Public Works Department**  
 102 Roadrunner Drive Sedona, AZ 86336  
 (928) 204-7111 • Fax: (928) 282-5348

**WW-01D - WW Collection System Improvements - Misc. Rehabs/Replacements**

**FY24 CIP Update**

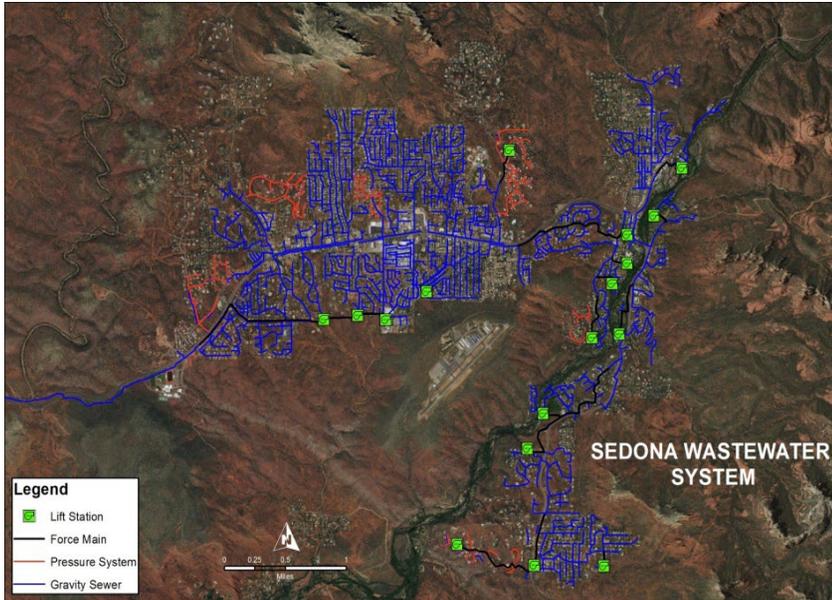

**KEY FEATURES:**

**Consultant:** ADC Wastewater Engineering

**Contractor:** TBD

**Timing:** FY24- FY25

**Construction Challenges:**

- Potential by-pass operations
- Securing existing services
- Material availability

**Project Manager:**

Roxanne Holland, PE  
 (928) 203-5069

[RHolland@SedonaAZ.gov](mailto:RHolland@SedonaAZ.gov)

**City Engineer:**

Kurtis Harris, PE  
 (928) 203-5059

[KHarris@SedonaAZ.gov](mailto:KHarris@SedonaAZ.gov)

**\$ FY24 Project Budget:** \$240,000

**Total Project Budget:** \$460,000

The 2017 Wastewater Master Plan Update (WWMP) included both condition assessments of existing sewer infrastructure and capacity analysis of the sewer collection system. During the desktop condition assessment, several pipes were identified as having issues such as deteriorated pipe lining, offset joints, cracks in the pipe, and general deterioration from hydrogen sulfide gasses.

This project will install pipe lining in Foothills Drive and El Camino Road, replace a portion of the 6-inch main line in Northview Road, and repair offset joints and re-line the 8-inch mains in Lazy Bear Estates.

**Status:** Design for the Northview Road sewer replacement is complete. Staff will advertise for bids for construction in April 2024 and construction is anticipated to begin in Spring 2024. Design for Foothills Drive, El Camino Road, and Lazy Bear estates is underway and expected to be complete Spring 2024.

**Project Status** **March 2024**

Project Phase	% Completion	Completion Date
Design	70%	Winter 2024
Construction	0%	Fall 2024
