




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

PT-01 - Transit Maintenance/Operations Center

FY24 CIP Update

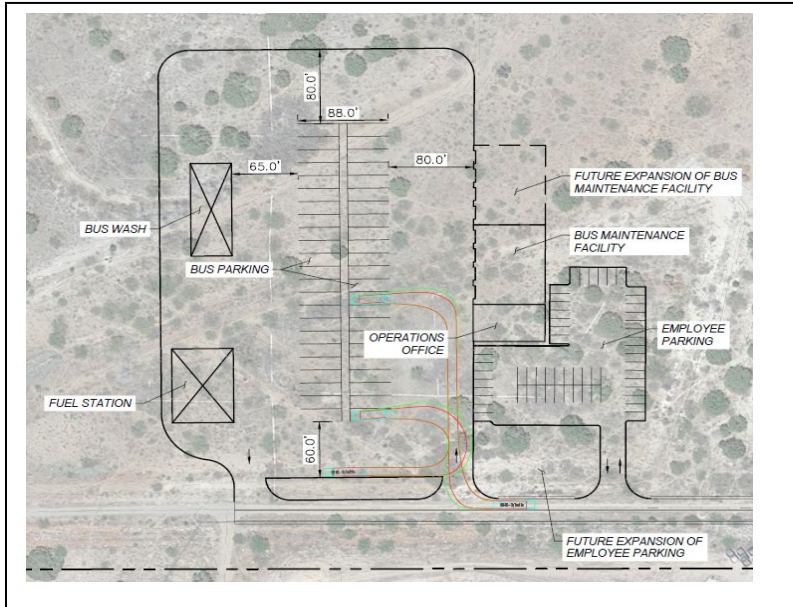

KEY FEATURES:

Consultant: To be determined

Contractor: To be determined

Timing: FY24 to FY27

Construction Challenges:

- Design leading to eventual "Zero Emissions" transit system.
- Existing WWRP piping to be rerouted

Project Manager:

Johnathan Hoffman
 (928) 203 – 5124
JHoffman@SedonaAZ.gov

City Engineer:

Kurt Harris, PE
 (928) 203-5039
KHarris@SedonaAZ.gov

\$ FY24 Project Budget: \$200,000
FY25 Project Budget: \$520,000
Total Project Budget: \$25,295,831

The Sedona Area Transit Implementation Plan (January, 2020) was completed with recommendations on phased fixed route bus services, demand response and shuttle services to various trailheads throughout the City and surrounding national forest. The City and its Verde Valley stakeholders are actively working to develop appropriate bus transit services as per the adopted plan. The Maintenance and Operations Facility development is part of the city's plan to support and enhance the transit services in the region. The completion of this Project will provide the required transit staff with all the space and equipment necessary to properly administer, operate and maintain the City's buses, as well as providing maintenance services to other transit systems in the Verde Valley.

The concept design and NEPA environmental studies have been completed for this project. The final design RFQ is currently under review by the Arizona Department of Transportation, as partial funding will be provided by grants from the Federal Transit Administration.

Project Status

May 2024

Project Phase	% Completion	Completion Date
Final Design	0%	March 2026
Construction	0%	FY27
