




City of Sedona
Public Works Department
 102 Roadrunner Drive Sedona, AZ 86336
 (928) 204-7111 • Fax: (928) 282-5348

WW-01D - WW Collection System Improvements - Misc. Rehabs/Replacements

FY25 CIP Update

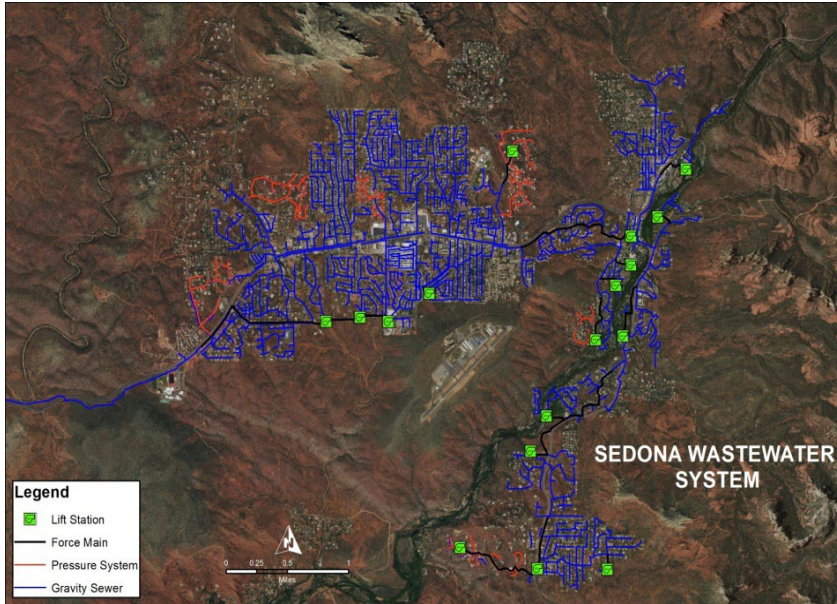

KEY FEATURES:

Consultant: ADC Wastewater Engineering

Contractor: TBD

Timing: FY24- FY25

Construction Challenges:

- Potential by-pass operations
- Securing existing services
- Material availability

Project Manager:

Roxanne Holland, PE
 (928) 203-5069

RHolland@SedonaAZ.gov

City Engineer:

Kurtis Harris, PE
 (928) 203-5059

KHarris@SedonaAZ.gov

\$ FY25 Project Budget: \$401,000

The 2017 Wastewater Master Plan Update (WWMP) included both condition assessments of existing sewer infrastructure and capacity analysis of the sewer collection system. During the desktop condition assessment, several pipes were identified as having issues such as deteriorated pipe lining, offset joints, cracks in the pipe, and general deterioration from hydrogen sulfide gasses.

This project will install pipe lining in Foothills Drive and El Camino Road, replace a portion of the 6-inch main line in Northview Road, and repair offset joints and re-line the 8-inch mains in Lazy Bear Estates.

Status: Design for the Northview Road sewer replacement is complete. Staff is in the process of notifying affected property owners. The project is anticipated to be advertised for bid in August 2024 for construction in fall 2024.

Design for the point repairs in Foothills Drive and El Camino Road is also complete. The project is anticipated to be advertised for bid in August 2024 for construction in fall 2024.

PROJECT STATUS

JULY FY25

Project Phase	% Completion	Completion Date
Design	100%	Winter 2023
Construction	0%	Fall 2024
