




**City of Sedona**  
**Public Works Department**  
 102 Roadrunner Drive Sedona, AZ 86336  
 (928) 204-7111 • Fax: (928) 282-5348

**WW-01D - WW Collection System Improvements - Misc. Rehabs/Replacements**

**FY25 CIP Update**

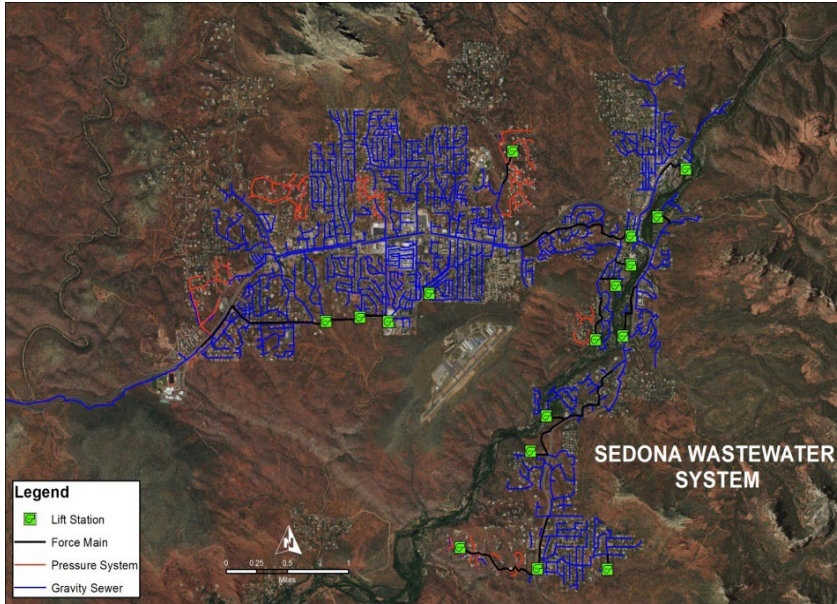

**KEY FEATURES:**

**Consultant:** ADC Wastewater Engineering

**Contractor:** TBD

**Timing:** FY24- FY25

**Construction Challenges:**

- Potential by-pass operations
- Securing existing services
- Material availability

**Project Manager:**

Roxanne Holland, PE  
 (928) 203-5069

[RHolland@SedonaAZ.gov](mailto:RHolland@SedonaAZ.gov)

**City Engineer:**

Kurtis Harris, PE  
 (928) 203-5059

[KHarris@SedonaAZ.gov](mailto:KHarris@SedonaAZ.gov)

**\$ FY25 Project Budget:** \$401,000

The 2017 Wastewater Master Plan Update (WWMP) included both condition assessments of existing sewer infrastructure and capacity analysis of the sewer collection system. During the desktop condition assessment, several pipes were identified as having issues such as deteriorated pipe lining, offset joints, cracks in the pipe, and general deterioration from hydrogen sulfide gasses.

This project will install pipe lining in Foothills Drive and El Camino Road, replace a portion of the 6-inch main line in Northview Road, and repair offset joints and re-line the 8-inch mains in Lazy Bear Estates.

**Status:** Design for the Northview Road sewer replacement is complete. Staff is in the process of notifying affected property owners. The project is anticipated to be advertised for bid in the fall 2024 with construction occurring fall/winter 2024-2025.

Design for the point repairs in Foothills Drive and El Camino Road is also complete. The project is anticipated to be advertised for bid in the fall 2024 with construction occurring fall/winter 2024-2025.

**PROJECT STATUS** **SEPTEMBER FY25**

Project Phase	% Completion	Completion Date
Design	100%	Winter 2023
Construction	0%	Fall/Winter 2024
